



**Okeehlee Middle School Classroom Additions  
 2200 Pinehurst Drive  
 Greenacres, Florida 33413  
 SDPBC Project No. 2151-8307  
 February 1, 2007**

**Table of Contents**

Transmittal Letter

Tab 1 ..... GMP Estimate Summary

Tab 2 ..... Construction Phase Fee

Tab 3 ..... General Conditions

Tab 4 ..... Plan and Specifications Listing

Tab 5 ..... GMP Qualifications and Clarifications

Tab 6 ..... Exhibits B, C, D, E, F, I, S

Tab 7 ..... M/WBE Certificates

Tab 8 ..... Subcontractor State Licenses

Tab 9 ..... Beneficial Interest and Disclosure of Ownership document and Trench Safety Act

Tab 10 ..... Project Schedule

Tab 11 ..... Value Engineering

622 Banyan Trail ♦ Suite 300 ♦ Boca Raton, Florida 33431 ♦ Phone (561) 361-6700 ♦ Fax (561) 361-6979

GREATER BOCA RATON CHAMBER OF COMMERCE

**BUSINESS OF THE YEAR 2005**

[www.kaufmanlynn.com](http://www.kaufmanlynn.com) ♦ CGC# 021732



February 1, 2007

The School District of Palm Beach County  
Program Management  
3300 Forest Hill Blvd. C-331  
West Palm Beach, FL 33406

Attn: Mr. James Cartmill  
Senior Projects Administrator

Re: Okeehoelee Middle School Classroom Addition  
2151-8307  
Letter of Transmittal

Mr. Cartmill:

Please find enclosed our Guaranteed Maximum Price submittal for the Okeehoelee Middle School Classroom Addition, SDPBC Project No 2151-8307. Our Guaranteed Maximum Price for this project is: **Seven Million Four Hundred Forty Eight Thousand Six Hundred Eighty Nine Dollars and No Cents (\$7,448,689).**

This GMP is based on the documents as prepared by ACAI Associates, Incorporated. Included in this submittal are our GMP estimate summary, plan and specifications listings, GMP Qualifications and Clarifications, and the required Exhibits. If you have questions or require any other clarification relating to this documentation please do not hesitate to contact me personally.

Sincerely,

Michael I Kaufman  
President  
Kaufman Lynn, Inc. General Contractors

622 Banyan Trail ♦ Suite 300 ♦ Boca Raton, Florida 33431 ♦ Phone (561) 361-6700 ♦ Fax (561) 361-6979

GREATER BOCA RATON CHAMBER OF COMMERCE  
**BUSINESS OF THE YEAR 2005**

[www.kaufmanlynn.com](http://www.kaufmanlynn.com) ♦ CGC# 021732

TAB 1

**Project: Okecheelee Middle School Classroom Addition - GMP**

**Architect:** ACAI Associates

**Date:** February 1, 2007

**Bldg SF New:** 40,689

**Bldg SF Reno:** -

**Total SF Active** 40,689

**Weeks** 52

**Months** 12.0

**Estimator:** Tom Kosier

<b>Id#</b>	<b>Description</b>	<b>Quantity</b>	<b>Unit</b>	<b>Unit Price</b>	<b>GMP Amount</b>	<b>W/MBE</b>	<b>Comments/Division Totals</b>
<b>02-000</b>	<b>SITE WORK</b>				<b>\$</b>		<b>636,505</b>
02-050	Demolition - Sidewalks & Tower	1	ls	49,995.00	\$ 49,995	-	DH Griffin
02-055	Misc Underground Conduit, Irrigation, Landscaping Demo	1	ls	10,000.00	\$ 10,000	-	Misc. U/G Utility Allowance
02-070	Surveying - Civil Scope of Work	1	ls	5,280.00	\$ 5,280	5,280	Brown & Phillips
02-070	Surveying - Building Scope of Work	1	ls	9,015.00	\$ 9,015	9,015	Brown & Phillips
02-100	Sitework Package	1	ls	343,480.00	\$ 343,480	-	Hughes
02-105	Turfblock Pavers @ Emergency Vehicle Access Road	17,820	sf	0.00	\$ -	-	N.I.C.
02-122	Temp. Fencing	2,400	lf	0.00	\$ -	-	Separate Contract
02-123	Dust Protection	2,400	lf	0.00	\$ -	-	Separate Contract
02-125	Site Logistics & Restoration Inc Bike Rack Relocation	1	ls	82,375.00	\$ 82,375	-	Cobra Construction
02-500	Paving & Surfacing - Asphalt Restoration	1	ls	0.00	\$ -	-	In Hughes
02-500	Temporary Access Roads	1	ls	1,000.00	\$ 1,000	-	KLJ
02-500	Roadway Maintenance During Construction	1	ls	3,500.00	\$ 3,500	-	KLJ
02-670	Drainage & Mobilization	1	ls	0.00	\$ -	-	In Hughes
02-700	Water Service	1	ls	0.00	\$ -	-	In Hughes
02-720	Sewer Service	1	ls	0.00	\$ -	-	In Hughes
02-800	New Ornamental Fence/Gates & 6'-0" CL fence @ bike rack	1	ls	36,300.00	\$ 36,300	36,300	Tropic Fence
02-900	Landscaping - Trees, Plants, Sod, Root Barrier	1	ls	55,935.00	\$ 55,935	55,935	Landscape Svc Pro
02-920	Irrigation	1	ls	39,625.00	\$ 39,625	-	IRF
02-960	Soils/ Density Testing	1	ls	0.00	\$ -	-	By Owner
02-965	Engineer's Testing/ Inspections	1	ls	0.00	\$ -	-	By Owner
02-970	Sod	37,200	sf	0.00	\$ -	-	In 02-900
<b>03-000</b>	<b>CONCRETE</b>				<b>\$</b>		<b>1,047,790</b>
03-090	Concrete Package - Tilt Up Wall Construction - 10" average thickness	1	ls	1,047,790.00	\$ 1,047,790	-	Drawdy Brothers
03-090	Form Liner Thin Brick Veneer	1	ls	0.00	\$ -	-	In Drawdy
03-090	Concrete Package - Chiller Plant Stand / No Roof	1	ls	0.00	\$ -	-	In Drawdy
03-090	Concrete Package - Covered Canopy Walkway	1	ls	0.00	\$ -	-	In Drawdy
03-330	Soil Poisoning	1	ls	0.00	\$ -	-	In Drawdy
03-350	Sidewalks	3,000	sf	0.00	\$ -	-	In Drawdy
<b>04-000</b>	<b>MASONRY</b>				<b>\$</b>		<b>-</b>
<b>05-000</b>	<b>METALS</b>				<b>\$</b>		<b>538,980</b>
05-015	Misc. Metals Package - Stairs, Railings, etc.	1	ls	0.00	\$ -	-	ISF
05-100	Structural Steel Package - Classroom Building	1	ls	538,980.00	\$ 538,980	457,950	ISF
	Panel to Panel & Panel to Footing Material	1	ls	0.00	\$ -	-	ISF



Id#	Description	Quantity	Unit	Unit Price	GMP Amount	W/MBE	Comments/Division Totals
<b>06-000</b>	<b>WOOD &amp; PLASTICS</b>						<b>\$ 270,741</b>
06-010	Carpentry Subcontract	38,625	sf	0.25 \$	9,656 \$		KLJ
06-400	Built-in Workstations, Counters, Cabinets, etc.	1	ls	241,085.00 \$	241,085 \$		Institutional Products
06-800	Classroom Building - Exterior Framing & Sheathing for Mfl Panels	1	ls	20,000.00 \$	20,000 \$		SPD
06-800	Classroom Building - Metal Trusses, Installation, Plywood Sheathing	1	ls	0.00 \$	- \$		In SPD
<b>07-000</b>	<b>THERMAL/MOISTURE PROTECTION</b>						<b>\$ 290,465</b>
07-100	Waterproofing - Elevator Pit & Concrete Eyebrows (Not Shown)	1	ls	1,350.00 \$	1,350 \$		Coman
07-200	Insulation	1	ls	0.00 \$	- \$		In Drywall Trade
07-250	Spray-On Fireproofing	1	ls	0.00 \$	- \$		N / A
07-270	Firestopping - Misc	1	ls	3,160.00 \$	3,160 \$		All States
07-500	Membrane Roofing - 20 yr NDL, Fire Rated Cap Sheet, 4 ply	194	sq	733.45 \$	142,290 \$		Triple M Roofing
07-505	Lightweight Concrete	19,400	sf	3.24 \$	62,890 \$		Don Works
07-525	Metal Roof & Fascia Panels	4,320	sf	15.27 \$	65,985 \$		Aeicor
07-725	Roof Hatch / With Ladder Up Post	1	ea	0.00 \$	- \$		In Triple M
07-900	Joint Sealers	1	ls	14,790.00 \$	14,790 \$		Coman
<b>08-000</b>	<b>DOORS &amp; WINDOWS</b>						<b>\$ 273,690</b>
08-100	Metal Doors & Frames	1	ls	113,205.00 \$	113,205 \$		Arc One / Firedoor
08-200	Wood & Plastic Doors	1	ls	0.00 \$	- \$		In Arc One / Firedoor
08-210	Finish Hardware	100	ea	0.00 \$	- \$		In Arc One / Firedoor
08-210	Knox Box	2	ea	650.00 \$	1,300 \$		KLJ
08-150	Doors/Frames/Hardware Labor	100	ea	125.50 \$	12,550 \$		HRC
08-900	Special Windows (Lite Kits at Misc Doors)	1	ls	0.00 \$	- \$		In Sol-A-Trol
08-900	Interior Glazing @ Reception Room 3-116	180	sf	0.00 \$	- \$		In Sol-A-Trol
08-900	Windows - Operable Casement Windows @ All Openings	1	ls	146,635.00 \$	146,635 \$		Sol-A-Trol
<b>09-000</b>	<b>FINISHES</b>						<b>\$ 655,805</b>
09-050	Drywall Package - Includes insulation @ interior & perimeter walls	1	ls	363,120.00 \$	363,120 \$		Atlantic Interiors
09-200	Stucco Exterior & Interior	1	ls	18,000.00 \$	18,000 \$		SPD
09-300	Tile Flooring	1	ls	59,870.00 \$	59,870 \$		Pallais
09-500	Acoustical Ceilings - 2x4 Cortega 770	36,575	sf	1.60 \$	58,430 \$		Superior Interiors
09-790	VCT/ Base	36,575	sf	1.85 \$	67,550 \$		Brookside
09-860	Floor Preparation	40,689	sf	0.35 \$	14,400 \$		Brookside
09-900	Painting Package	1	ls	74,435.00 \$	74,435 \$		Gray's Painting
09-910	Painting - Exterior	1	ls	- \$	- \$		Gray's Painting
09-950	Wall Covering/Vinyl	1	ls	- \$	- \$		NIC

Id#	Description	Quantity	Unit	Unit Price	GMP Amount	W/MBE	Comments/Division Totals
<b>10-000</b>	<b>SPECIALTIES</b>				\$		<b>115,000</b>
10-050	Appliances - Dishwasher & Refrigerator @ 3-208A	1	ls	2,500.00	\$ 2,500		Allowance
10-055	Corner Guards - Supply & Install	100	ea	44.40	\$ 4,440		C/S Group & KLI
10-075	Electric Pencil Sharpeners	25	ea	40.00	\$ 1,000		KLI
10-100	Tack Boards - Various Sizes	54	ea	190.63	\$ 15,250		Florida Chalkboard
10-100	Marker Board w/ Map & Chalk Rail - 16 x 4	26	ea	0.00	\$ -		In Florida Chalkboard
10-105	GPS Clocks	29	ea	0.00	\$ -		In Electrician
10-110	Exterior Plaques	0	ea		\$ -		In Full Moon
10-110	Display Cases - 4 x 6 units By Claridge	1	ea	2,050.00	\$ 2,050		Florida Chalkboard
10-200	Louvers/ Vents	7	ea	1,135.71	\$ 7,950		GC Bldg Products
10-350	Flagpoles	0	ea		\$ -		NIC
10-375	Bicycle Racks	0	ea		\$ -		NIC
10-500	Lockers	0	ea		\$ -		NIC
10-532	Aluminum Walkway Canopy	621	sf	21.78	\$ 13,525		NIC
10-520	Fire Extinguishers -	1	ls	3,565.00	\$ 3,565		Walker Design
10-655	Toilet Partitions	14	ea	1,031.43	\$ 14,440		Triangle
10-670	Storage Shelving	1	ls	28,750.00	\$ 28,750		Elechs
10-800	Toilet/Bath Accessories	1	ls	9,240.00	\$ 9,240		List Industries
10-950	Signage - Interior Doors	1	ls	12,290.00	\$ 12,290		Elechs
						12,290	Full Moon Over Florida
<b>11-000</b>	<b>EQUIPMENT</b>				\$		<b>3,900</b>
11-130	LCD Projector & Mount (PBCSB Dictated Allowance)	25	ea	0.00	\$ -		NIC
11-130	Projection Screens - 6'6"x4'h (Manual Pull Down, Wall Mtd)	25	ea	156.00	\$ 3,900		Florida Chalkboard
11-130	DVD/VCR Combo Unit (PBCSB Dictated Allowance)	25	ea	0.00	\$ -		NIC
11-130	Sound Field Enhancement Equipment (PBCSB Dictated Allowance)	25	ea	0.00	\$ -		NIC
11-130	Document Camera (PBCSB Dictated Allowance)	25	ea	0.00	\$ -		NIC
11-130	ITV/Future Equipment (By PBCSB)	0	ea	0.00	\$ -		NIC
11-130	Wireless Laptop Cart (By PBCSB)	0	ea	0.00	\$ -		NIC
11-130	Computers (By PBCSB)	0	ea	0.00	\$ -		NIC
11-130	Printers/Scanners (By PBCSB)	0	ea	0.00	\$ -		NIC
<b>12-000</b>	<b>FURNISHINGS</b>				\$		<b>62,310</b>
12-345	Chemistry Lab Equipment & Casework	1	ls	56,965.00	\$ 56,965		Newton
12-500	Window Treatments - Vertical Blinds	1,840	sf	2.90	\$ 5,345		Nat'l Stage & Window
<b>13-000</b>	<b>SPECIAL CONSTRUCTION</b>				\$		
<b>14-000</b>	<b>CONVEYING SYSTEMS</b>				\$		<b>53,400</b>
14-200	Elevators - Holeless Hydraulic, Std Cab	1	ls	53,400.00	\$ 53,400		Thyssenkrupp
<b>15-000</b>	<b>MECHANICAL</b>				\$		<b>1,128,675</b>
15-300	Fire Protection - Bldg Service	40,689	sf	3.05	\$ 123,930		Farmer & Irwin
15-300	Fire Protection - Flow Test	1	ls		\$ -		N.I.C.
15-400	Plumbing	80	uts	2,426.81	\$ 194,145		Farmer & Irwin
15-500	H.V.A.C. - 165 ton Chiller Plant	1	ls	810,600.00	\$ 810,600		Farmer & Irwin
15-500	Acoustical Sound Panels @ Chiller Yard	1	ls	0.00	\$ -		Farmer & Irwin

Id#	Description	Quantity	Unit	Unit Price	GMP Amount	W/MBE	Comments/Division Totals
<b>16-000</b>	<b>ELECTRICAL</b>						<b>\$ 949,000</b>
16-050	Basic Electrical - Fixtures, Gear, Wiring & New Service	40,689	sf	23.32	\$ 949,000		\$ - Fastrac
16-050	Basic Electrical - Chiller Plant	1	IS		\$ -		\$ - In Fastrac
16-200	Generators	0	IS		\$ -		\$ - N/A
16-500	Lighting	1	IS		\$ -		\$ - In Fastrac
16-600	Special Systems - Security (Empty Conduits Only)	1	IS		\$ -		\$ - In Fastrac
16-600	Special Systems - Card Access Conduit & Wire	3	ea		\$ -		\$ - In Fastrac
16-600	Special Systems - Video Surveillance (Empty Conduits Only)	1	IS		\$ -		\$ - In Fastrac
16-600	Special Systems - EMCS (Empty Conduits Only)	1	IS		\$ -		\$ - In Fastrac
16-600	Special Systems - Phones (Empty Conduits Only)	1	IS		\$ -		\$ - In Fastrac
16-600	Special Systems - Data & Voice (Empty Conduits Only)	1	IS		\$ -		\$ - In Fastrac
16-600	Special Systems - Master TV & Antenna (Empty Conduits Only)	1	IS		\$ -		\$ - In Fastrac
16-710	Intercom System	1	IS		\$ -		\$ - In Fastrac
16-750	Lightning Protection & TVSS	1	IS		\$ -		\$ - In Fastrac
16-800	Fire Alarms	1	IS		\$ -		\$ - In Fastrac
<b>HARD BUDGETS COSTS</b>							
<b>DIVISION 1 GENERAL REQUIREMENTS (Direct Cost Related to Site)</b>					<b>\$ 6,026,261</b>		<b>\$ 6,026,261</b>
<b>CONSTRUCTION PHASE FEE</b>					<b>11,110</b>		
<b>GENERAL CONDITIONS (Direct Cost Related to Field Staff)</b>					<b>592,821</b>		
<b>SUBTOTAL</b>					<b>253,351</b>		
<b>MANAGEMENT FEE</b>					<b>6,883,543</b>		
<b>SUBTOTAL</b>					<b>378,595</b>		
<b>GENERAL LIABILITY INSURANCE</b>					<b>7,262,138</b>		
<b>SUBTOTAL</b>					<b>-</b>		<b>NIC</b>
<b>BUILDERS RISK INSURANCE</b>					<b>7,262,138</b>		
<b>SUBTOTAL</b>					<b>-</b>		<b>NIC</b>
<b>PAYMENT &amp; PERFORMANCE BOND</b>					<b>7,262,138</b>		
<b>SUBTOTAL</b>					<b>66,026</b>		
<b>OWNER'S ARCHITECTURAL DESIGN CONTINGENCY</b>					<b>7,328,164</b>		
<b>CONTINGENCY</b>					<b>-</b>	<b>0.00%</b>	
<b>SALES TAX RECOVERY</b>					<b>180,788</b>	<b>3.00%</b>	
<b>GUARANTEED MAXIMUM PRICE TOTAL</b>					<b>(60,263)</b>	<b>-1.00%</b>	
					<b>7,448,689</b>	<b>\$ 1,217,375</b>	<b>16.34%</b>

TAB 2

<b>Project:</b>		<b>Okeehelée Middle School Addition</b>		<b>Date:</b>		February 1, 2007		SF New structures		
		<b>Summary of Construction Phase Fee</b>		<b>Bldg SF:</b>		40,689		SF Renovation		
				<b>Duration:</b>		40,689		SF Total		
						52		Wks		
						12.0		Mos		
<b>Id#</b>	<b>Description</b>	<b>Quantity</b>	<b>Unit</b>	<b>Unit Price</b>	<b>Const. Fee / Staff</b>	<b>Comments/Division Totals</b>				
<b>GENERAL REQUIREMENTS</b>										
01-900	Superintendent	52	wks	3,200.00	\$	100%	3,200	100%	166,400	
01-910	Project Engineer - MWBE - CM	52	wks	1,821.35	\$	100%	1,821	100%	94,710	
01-915	Project Accounting	52	wks	455.34	\$	25%	1,821	25%	23,659	
01-920	Project Coordinator	52	wks	910.68	\$	50%	1,821	50%	47,319	
01-960	Project Manager	52	wks	3,145.96	\$	100%	3,146	100%	163,464	
01-975	Senior Project Manager	52	wks	1,320.00	\$	33%	4,000	33%	68,587	
01-976	Project Executive	52	wks	552.00	\$	5%	0	5%	28,682	
<b>Total Construction Phase Fee</b>					<b>\$</b>				<b>592,821</b>	

TAB 3

**Project:** Okechee Middle School Addition  
 Summary of General Conditions


**Date:** February 1, 2007  
**Bldg SF:** 40,689  
**Duration:** 52 Wks  
 12.0 Mos

SF New structures  
 SF Renovation  
 SF Total  
 Wks  
 Mos

Id#	Description	Quantity	Unit	Unit Price	Total	Comments/Division Totals
<b>01-000</b>	<b>GENERAL REQUIREMENTS</b>					
01-010	Background/Security Check	1	ls	5,000.00	\$ 5,000	
01-045	Job Site Trailer	12	mo	600.00	\$ 7,200	
	Set up and Removal	2	ls	2,400.00	\$ 4,800	
	Owner's Trailer	12	mo	600.00	\$ 7,200	
	Furniture - Owner's Equipment - Allowance	1	mo	5,000.00	\$ 5,000	<b>Allowance</b>
01-085	Postage	12	mo	500.00	\$ 6,000	
01-100	Storage Containers	12	mo	200.00	\$ 2,400	
01-225	Safety Consultant - Inspections - OSHA Certified	12	mo	490.00	\$ 5,880	
01-310	Blueprints	1	ls	5,500.00	\$ 5,500	
01-312	Job Photos	12	mo	125.00	\$ 1,500	
01-320	As-Built Drawings	1	ls	3,000.00	\$ 3,000	
01-322	Close Out Documents	1	ls	1,500.00	\$ 1,500	
01-325	Office Accessories	12	mo	500.00	\$ 6,000	
01-326	Jobsite Office Equipment	1	ls	5,200.00	\$ 5,200	
01-500	Temporary Phone	12	mo	250.00	\$ 3,000	
	Telephone Install	1	ls	1,500.00	\$ 1,500	
	Trades Telephone	12	mo	400.00	\$ 4,800	
01-505	Computer Expenses, DSL Set Up, Job Camera	1	ls	5,680.00	\$ 5,680	
	Computer Network	12	mo	750.00	\$ 9,000	
01-515	Cell Phones/Radios / Nextel	12	mo	795.00	\$ 9,540	
01-520	Temporary Toilets (2 Units)	12	mo	650.00	\$ 7,800	
01-530	Temporary Electric - Office Trailers	12	mo	400.00	\$ 4,800	
	Temporary Electric - Building Construction	12	mo	600.00	\$ 7,200	
	Temp Electric Install Building & Office Trailer Set Up	1	ls	1,500.00	\$ 1,500	
01-535	Temporary A/C	4	mo	6,000.00	\$ 24,000	
01-540	Temporary Water	12	mo	125.00	\$ 1,500	
	Temp Water Install	1	ls	650.00	\$ 650	
	Elevator Cab Protection & Maintenance	1	ls	2,500.00	\$ 2,500	
	Traffic Control	12	mo	250.00	\$ 3,000	
01-550	Trash Removal - Dumpster	75	ea	475.00	\$ 35,625	
01-560	Gas, Oil, Trucks	12	mo	1,200.00	\$ 14,400	
01-601	First Aid Kit	1	ls	250.00	\$ 250	
01-710	Final Cleaning - Sub	40,689	sf	0.30	\$ 12,207	
01-800	Construction Clean - Materials	1	ls	500.00	\$ 500	
01-810	Construction Clean-Up Labor (1/2 Duration)	26	wks	480.00	\$ 12,470	
01-850	Misc. Tools & Equipment	12	mo	500.00	\$ 6,000	
01-980	Ice & Water / Water Cooler Rental	52	wks	25.00	\$ 1,299	
01-995	Job Sign	1	ls	1,750.00	\$ 1,750	
01-997	Project Signage (Directional - Interior & Exterior)	1	ls	1,200.00	\$ 1,200	
	Building Envelope Consultant Review	1	ls	5,000.00	\$ 5,000	
	Warranties - Supervision & Coordination Costs For Warranty Work	1	ls	10,000.00	\$ 10,000	In Estimate Line Item
	<b>Total General Conditions</b>				\$ <b>253,351</b>	

TAB 4





**Okeehelée Middle School Classroom Additions**  
**2200 Pinehurst Drive**  
**Greenacres, Florida 33413**  
**SDPBC Project No. 2151-8307**  
**February 1, 2007**

**LIST OF DOCUMENTS**

**GENERAL DRAWINGS**

G0.1	Cover Sheet and Drawing Index	11/03/2006
1 of 2	Topographic Survey	06/02/2006
2 of 2	Topographic Survey	06/02/2006

**CIVIL DRAWINGS**

C-0	Cover Sheet	Stamped 11/13/2006
C-1	General Notes and Specifications	Stamped 11/13/2006
C-2	Grading and Drainage Plan	11/02/2006
C-3	Water and Sanitary Sewer Plan	11/20/2006
C-4	Grading and Drainage Details	Stamped 11/13/2006
C-5	Standard Water Details	Stamped 11/13/2006
C-6	Standard Sewer Details	Stamped 11/13/2006
C-7	Water & Wastewater Details	No Date
C-8	Wastewater Details	No Date

**LANDSCAPE DRAWINGS**

LP-1	Landscape Plan	11/28/2006
LP-2	Landscape Plan	11/28/2006
LP-3	Landscape Plan	11/28/2006
IR-1	Irrigation Plan	11/14/2006
IR-2	Irrigation Plan	11/14/2006
IRD-3	Irrigation Details	11/14/2006
IRN-4	Irrigation Notes	11/14/2006

**ARCHITECTURAL DRAWINGS**

A0.0	Overall Site Plan and Code Analysis	11/03/2006
A0.1	Site Plan and Canopy Details	11/03/2006
LS.1	First Floor – Life Safety Plan	11/03/2006
LS.2	Second Floor – Life Safety Plan	11/03/2006
A1.1	First Floor Plan	11/03/2006
A1.2	Second Floor Plan	11/03/2006
A2.1	Roof Plan and Details	11/03/2006

## **ARCHITECTURAL DRAWINGS Continued**

A3.1	First Floor – Reflected Ceiling Plan	11/03/2006
A3.2	Second Floor – Reflected Ceiling Plan	11/03/2006
A4.1	Exterior Elevations	11/03/2006
A5.1	Building Sections	11/03/2006
A5.2	Wall Sections	11/03/2006
A5.3	Partition Types	12/04/2006
A5.4	General Details	11/03/2006
A6.1	Door Details and Schedule	11/03/2006
A6.2	Window and Louvers Details and Schedules	11/03/2006
A7.1	First Floor Furniture Layout Plan & Finish Sched.	11/03/2006
A7.2	Second Floor Furniture Layout Plan & Finish Sched.	11/03/2006
A7.3	Enlarged Furniture Plans and Interior Elevations	11/03/2006
A7.4	Enlarged Furniture Plans	11/03/2006
A7.5	Interior Elevations	11/03/2006
A7.6	Casework Elevations and Details	11/03/2006
A8.1	Enlarged Toilet Plans and Elevations	11/03/2006
A8.2	Enlarged Elevator Hoistway Sections and Details	11/03/2006
A8.3	Enlarged Stair #1 Sections and Details	11/03/2006
A8.4	Enlarged Stair #2 Sections and Details	11/03/2006
A8.5	Enlarged Stair #3 Sections and Details	11/03/2006
A9.1	Signage Plans	11/03/2006
A9.2	Signage Details	09/29/2006
A9.3	Signage Details	11/03/2006

## **STRUCTURAL DRAWINGS**

S1.0	General Notes	11/03/2006
S1.1	Foundation Plan	11/03/2006
S1.2	Second Floor Framing Plan	11/03/2006
S1.3	Roof Framing Plan	12/11/2006
S3.0	Structural Details and Schedules	11/03/2006
S3.1	Sections and Details	11/03/2006
S3.2	Sections and Details	11/03/2006
S3.3	Sections and Details	11/03/2006
S4.1	Wind Pressures	11/03/2006

## **MECHANICAL DRAWINGS**

M0-01	Legend, General Notes, and Schedules	08/14/2006
M0-02	Schedules	12/11/2006
M0-03	Schedules and Mechanical Site Plan	11/09/2006
M1-01	First Floor HVAC Plan	11/09/2006
M1-02	Second Floor HVAC Plan	11/09/2006
M2-01	Mechanical Room Plan and Sections	11/09/2006
M2-02	Chiller Yard and Piping Schematic	11/09/2006
M3-01	Mechanical Details	08/14/2006

## **MECHANICAL DRAWINGS Continued**

M3-02	Mechanical Details	08/14/2006
M4-01	Mechanical Controls	08/14/2006

## **ELECTRICAL DRAWINGS**

E0-01	Electrical Site Plan	11/09/2006
E1-01	First and Second Floor Plan – Lighting	11/09/2006
E1-02	First and Second Floor Plan – Power	11/09/2006
E1-03	First and Second Floor Plan – System	11/09/2006
E2-01	Enlarged Elec Rooms and Chiller Area	11/09/2006
E3-01	Riser Diagrams	12/07/2006
E4-01	Notes, Legend, and Fixture Schedule	08/14/2006
E4-02	Misc. Schedules and Panelboards	12/07/2006
E4-03	Panelboards	11/09/2006
E5-01	Miscellaneous Details	08/14/2006
E5-02	Miscellaneous Details	08/14/2006
E5-03	Miscellaneous Details	08/14/2006
E5-04	Miscellaneous Details	08/14/2006
E5-05	Miscellaneous Details	08/14/2006

## **PLUMBING DRAWINGS**

P0-01	Schedules, Legend and Notes	11/09/2006
P1-01	Plumbing Floor Plans	11/09/2006
P1-02	Plumbing Roof Plan	08/14/2006
P2-01	Enlarged Lab. and Riser Diagrams	11/09/2006

## **FIRE PROTECTION DRAWINGS**

FP0-01	Legend, General Notes, and Schedules	08/14/2006
FP1-01	First Floor Fire Protection Plan	08/14/2006
FP1-02	Second Floor Fire Protection Plan	08/14/2006
FP2-01	Fire Protection Details	08/14/2006

## **PROJECT SPECIFICATIONS**

### **INTRODUCTORY INFORMATION**

00001 – Title Page	11/17/2006
00010 – Project Manual Index	11/17/2006

### **DIVISION 1**

01010 – Summary of Work	11/17/2006
Geotechnical Report	06/05/2006
01027 – Applications for Payment	09/29/2006
01028 – Modification Requirements	09/29/2006
01039 – Coordination and Meetings	09/29/2006

01045 – Cutting and Patching	09/29/2006
01060 – Regulatory Requirements	09/29/2006
01120 – Alteration Projects Procedures	09/29/2006
01230 – Alternate Bid	11/17/2006
01300 – Submittals	09/29/2006
01311 – Network Analysis Schedules	09/29/2006
01400 – Quality Control	09/29/2006
01410 – Testing Laboratory Service	09/29/2006
01500 – Construction Facilities & Temporary Controls	09/29/2006
01540 – Security	09/29/2006
01560 – Temporary Controls	09/29/2006
01600 – Material Equipment and approved equals	09/29/2006
01650 – Starting of Systems	09/29/2006
01700 – Contract Closeout	09/29/2006
01730 – Operation & Maintenance Data	09/29/2006
01740 – Warranties	09/29/2006

**DIVISION 2**

02070 – Selective Demolition	09/29/2006
02110 – Site Clearing	09/29/2006
02200 – Earth Work	09/29/2006
02280 – Soil Treatment for Termite Control	09/29/2006
02400 – Bituminous Concrete Paving	09/29/2006
02520 – Concrete Curbs and Walks	09/29/2006
02565 – Liquid Petroleum Gas Storage & Distribution	11/17/2006
02580 – Pavement Marking	09/29/2006
02660 – Water Distribution System	09/29/2006
02685 – Gas Piping	11/17/2006
02700 – Storm Drainage System	09/29/2006
02730 – Sanitary Sewerage Collection System	09/29/2006
02800 – Site Improvements & Amenities	09/29/2006
02810 – Underground Irrigation System	09/29/2006
02825 – Ornamental Alum Fencing & Gates	09/29/2006
02831 – Chain Link Fence & Gate	09/29/2006
02938 – Grass Sodding	09/29/2006
02950 – Trees, Plants & Ground Cover	09/29/2006

**DIVISION 3**

03100 – Concrete Formwork	09/29/2006
03200 – Concrete Reinforcement	09/29/2006
03300 – Cast-in-place Concrete	11/17/2006
03346 – Concrete Floor Finishing	09/29/2006
03470 – Tilt-up Precast Concrete	09/29/2006
03521 – Insulating Concrete Fill	09/29/2006

**DIVISION 4**

04100 – Mortar & Grout 09/29/2006  
04300 – Unit Masonry System 09/29/2006

**DIVISION 5**

05120 – Structural Steel 09/29/2006  
05210 – Steel Joists 09/29/2006  
05310 – Steel Deck 09/29/2006  
05400 – Cold Formed Metal Framing 09/29/2006  
05500 – Metal Fabrications 09/29/2006  
05510 – Metal Stairs 09/29/2006  
05520 – Handrails and Railings 09/29/2006

**DIVISION 6**

06100 – Rough Carpentry 09/29/2006  
06410 – Custom Casework 09/29/2006

**DIVISION 7**

07120 – Fluid Applied Waterproofing 09/29/2006  
07160 – Bituminous Dampproofing 09/29/2006  
07170 – Bentonite Waterproofing 11/17/2006  
07181 – Water Repellent Penetrant 11/17/2006  
07212 – Extruded Polystyrene Board Insulation 09/29/2006  
07213 – Batt Insulation 09/29/2006  
07270 – Firestopping 09/29/2006  
07465 – Preformed Metal Siding 11/17/2006  
07536 – Modified Bitumen Roofing System 09/29/2006  
07610 – Standing Seam Metal Roofing 11/17/2006  
07620 – Sheet Metal Flashing & Trim 09/29/2006  
07724 – Roof Hatches 09/29/2006  
07900 – Joint Sealants 09/29/2006

**DIVISION 8**

08110 – Hollow Metal Doors & Frames 09/29/2006  
08210 – Solid Core Wood Doors 09/29/2006  
08305 – Access Doors/Hatches 09/29/2006  
08520 – Aluminum Windows 09/29/2006  
08710 – Finish Hardware 09/29/2006  
08800 – Glass and Glazing 09/29/2006

**DIVISION 9**

09111 – Metal Stud Framing System 09/29/2006  
09206 – Metal Furring & Lathing 09/29/2006  
09220 – Portland Cement Plaster 09/29/2006  
09250 – Gypsum Board System 09/29/2006

09311 – Ceramic Tile	09/29/2006
09511 – Suspended Acoustical Ceiling System	09/29/2006
09650 – Resilient Flooring	09/29/2006
09688 – Carpet Non-modular	09/29/2006
09900 – Painting	09/29/2006

**DIVISION 10**

10100 – Marker Boards & Tack Boards	09/29/2006
10171 – Toilet Compartments, Urinal Screens, Shower Cubicles	09/29/2006
10211 – Fixed Metal Wall Louvers	09/29/2006
10260 – Wall Protection System	09/29/2006
10415 – Display Cases	11/17/2006
10420 – Plaque	09/29/2006
10441 – Identifying Devices	09/29/2006
10522 – Fire Extinguishers, Cabinets & Accessories	09/29/2006
10532 – Aluminum Walkway Covers	09/29/2006
10675 – Metal Shelving	11/17/2006
10800 – Toilet & Bath Accessories	09/29/2006

**DIVISION 11**

11131 – Projection Screens	09/29/2006
----------------------------	------------

**DIVISION 12**

12345 – Chemistry Laboratory Casework & Equipment	11/17/2006
12500 – Window Vertical Blinds	09/29/2006
12692 – Surface Mounted Entrance Mats	09/29/2006

**DIVISION 14**

14245 – Hydraulic Elevators – Passenger	11/17/2006
---	------------

**DIVISION 15**

15000 – Basic Mechanical Requirements	07/28/2006
15073 – Minor Mechanical Demolition	07/28/2006
15135 – Liquid & Air Flow Meters, Gauges and Thermometers	07/28/2006
15140 – Supports, Bases and Anchors	07/28/2006
15170 – Motors	07/28/2006
15190 – Mechanical Identification	07/28/2006
15242 – Vibration Isolation	07/28/2006
15260 – Piping Insulation	07/28/2006
15280 – Equipment Insulation	07/28/2006
15290 – Ductwork Insulation	07/28/2006
15411R – Potable Water Systems	11/28/2006
15412R – Soil and Waste Systems	11/28/2006
15420R – Plumbing Piping	11/28/2006
15430R – Plumbing Specialties	11/28/2006

15440R – Plumbing Fixtures & Accessories	11/28/2006
15450R – Plumbing Equipment	11/28/2006
15500 – Fire Protection	07/28/2006
15510 – Hydronic Piping	07/28/2006
15515 – Hydronic Specialties	07/28/2006
15535 – Refrigeration Piping & Specialties	07/28/2006
15540 – HVAC Pumps	07/28/2006
15671 – Air Cooled Air Conditioning Condensing Units	07/28/2006
15682 – Air Cooled Water Chillers	07/28/2006
15765 – Variable Frequency Drive Units	07/28/2006
15801 – Water Treatment	07/28/2006
15817 – Electric Resistance Duct Heaters	07/28/2006
15855 – Air Handling Units	07/28/2006
15870 – Power Ventilators	07/28/2006
15885 – Air Filters	07/28/2006
15890 – Ductwork	07/28/2006
15895 – Ductwork Accessories	07/28/2006
15900 – Energy Management and Control System (Automated Logic)	07/28/2006
15930 – Variable Air Volume Terminal Units	07/28/2006
15936 – Grilles, Registers, Diffusers	07/28/2006
15990 – HVAC Systems	07/28/2006
15991 – TAB of HVAC Systems	07/28/2006
15992 – Tests – Piping Systems	07/28/2006

#### **DIVISION 16**

16010 – Basic Electrical Requirements	07/28/2006
16020 – Work Included	07/28/2006
16025 – Codes, Fees, and Standards	07/28/2006
16050 – Basic Materials and Methods	07/28/2006
16111 – Conduit	07/28/2006
16123 – Building Wire and Cable	07/28/2006
16130 – Boxes	07/28/2006
16141 – Wiring Devices	07/28/2006
16160 – Cabinets and Enclosures	07/28/2006
16180 – Equipment Wiring Systems	07/28/2006
16190 – Supporting Devices	07/28/2006
16195 – Electrical Identification	07/28/2006
16420 – Service Entrance	07/28/2006
16440 – Disconnect Switches	07/28/2006
16450 – Grounding	07/28/2006
16461 – Dry Type Transformers	07/28/2006
16470 – Panelboards	07/28/2006
16480 – Motor Controls	07/28/2006
16485 – Contactors	07/28/2006
16495 – Transfer Switch	07/28/2006
16510 – Interior Luminaries	07/28/2006

16535 – Emergency Lighting Equipment	07/28/2006
16610 – Transient Voltage Surge Suppression	07/28/2006
16650 – Energy Management and Control System	07/28/2006
16670 – Lightning Protection Systems	07/28/2006
16721 – Fire Alarm and Smoke Detection Systems	07/28/2006
16722 – Intrusion Detection and Security Access System	07/28/2006
16723 – Video Surveillance System	07/28/2006
16725 – Card Access System	07/28/2006
16730 – GPS Wireless Clock System	07/28/2006
16765 – Intercom System	07/28/2006
16770 – Public Address System	07/28/2006
16781 – Master Television Antenna System (MTAS)	07/28/2006
16902 – Electric Controls and Relays	07/28/2006
16905 – Communication System	07/28/2006
16906 – Ceiling Projector Raceway System	07/28/2006

**ARCHITECT RESPONSES TO RFI'S**

<u>RFI No.</u>	<u>RFI Title</u>
1	Emergency Road Details
2	Water/Sewer Conflict Tags
3	Irrigation System
4	Aluminum Canopy Foundations
5	Lab Equipment Manufacturers
6	ECMS Responsibilities
7	Low Voltage System Responsibilities/Clarifications
8	Alternate to Brick
9	Concrete Eyebrow Structural Details
10	Sidewalk Discrepancies
11	FDC Detail
12	Exterior Opening Design Pressures
13	Parapet Framing Details
14	Acoustical Ceilings 2x2 vs 2x4
15	Panel to Footing Steel Spacing
16	Brick Flashing
17	Science Room Furniture Tags
18	Science / Chemistry Lab Specification Clarification
19	Dishwasher & Refrigerator
20	Chemistry Lab Equipment
21	Roofing Layout Conflict
22	Teacher Work Stations
23	Elevator Capacity
24	Classroom sinks
25	Emergency eyewash/shower
26	2nd Floor Egress Windows
27	Science Demo Room Plumbing Fixtures
28	Window Details – Hollow Metal vs Aluminum @ Exterior Windows



TAB 5



**Okeehelée Middle School Classroom Additions  
2200 Pinehurst Drive  
Greenacres, Florida 33413  
SDPBC Project No. 2151-8307  
February 1, 2007**

**Specification Listing With Qualifications/Clarifications and Assumptions**

The following is a listing of specification sections by division with the applicable qualifications and assumptions that have been made relating to the 100% Construction Project Documents (plan listing attached) including revised documents listed in this section.

**DIVISION 1: GENERAL REQUIREMENTS**

1. Building permit fees, subcontractor permit fees, impact fees, or any deposits paid to any utility authority are to be paid for by the Owner.
2. Builder's Risk Insurance premiums and deductibles have not been included at this time. Builder's Risk Insurance to be provided by the Owner.
3. General Liability Insurance has not been included at this time as it is to be carried under the Owner's Insurance program.
4. The cost of temporary utilities tie in is included. Cost for the use of temporary utilities has been included however the cost of utilities for building systems after substantial completion has not been included.

**DIVISION 4: MASONRY**

1. We have not included any brick or form liner work at the 13 "typical" window areas as shown on the attached SK-1

**DIVISION 6: WOODS & PLASTICS**

1. We have not included the large Teacher Storage Cabinets (Item #10 on A7.4) in rooms 3-101, 3-102, 3-103, 3-104, 3-111, 3-112, 3-113, 3-114, 3-202, 3-204, 3-205, 3-211, 3-212, 3-213, 3-214, 3-215, 3-217, and 3-219 as per the District's plan review comments

## **DIVISION 8: DOORS AND WINDOWS**

1. Fire-rated doors in pairs or with vision lights do not maintain STC-30 ratings and are provided as “STC-30 construction” only to maintain the life safety requirements.
2. We have included the exterior windows as manufactured by Sol-A-Trol. Please note that the cam locks will receive a nickel bronze finish in lieu of the specified stainless steel as the product approval is based upon the nickel bronze material only.

## **DIVISION 10: SPECIALTIES**

1. We have included an allowance of \$2,500 for the refrigerator and dishwasher noted on the plans (A7.4) in room 3-208A. We have not included any other appliances at this time.
2. We have included the metal shelving at the rooms/locations as called out for in the plans as “Hi-Tech Industrial Shelving” as manufactured by List Industries.

## **DIVISION 15: MECHANICAL**


### **Fire Protection**

1. We have not received a flow test report for the fire sprinklers. We have assumed that the flow will be adequate at this time.

## **DIVISION 16: ELECTRICAL**

1. We have not included the relocation or installation of any new or existing ITV towers at this time.

SK-1

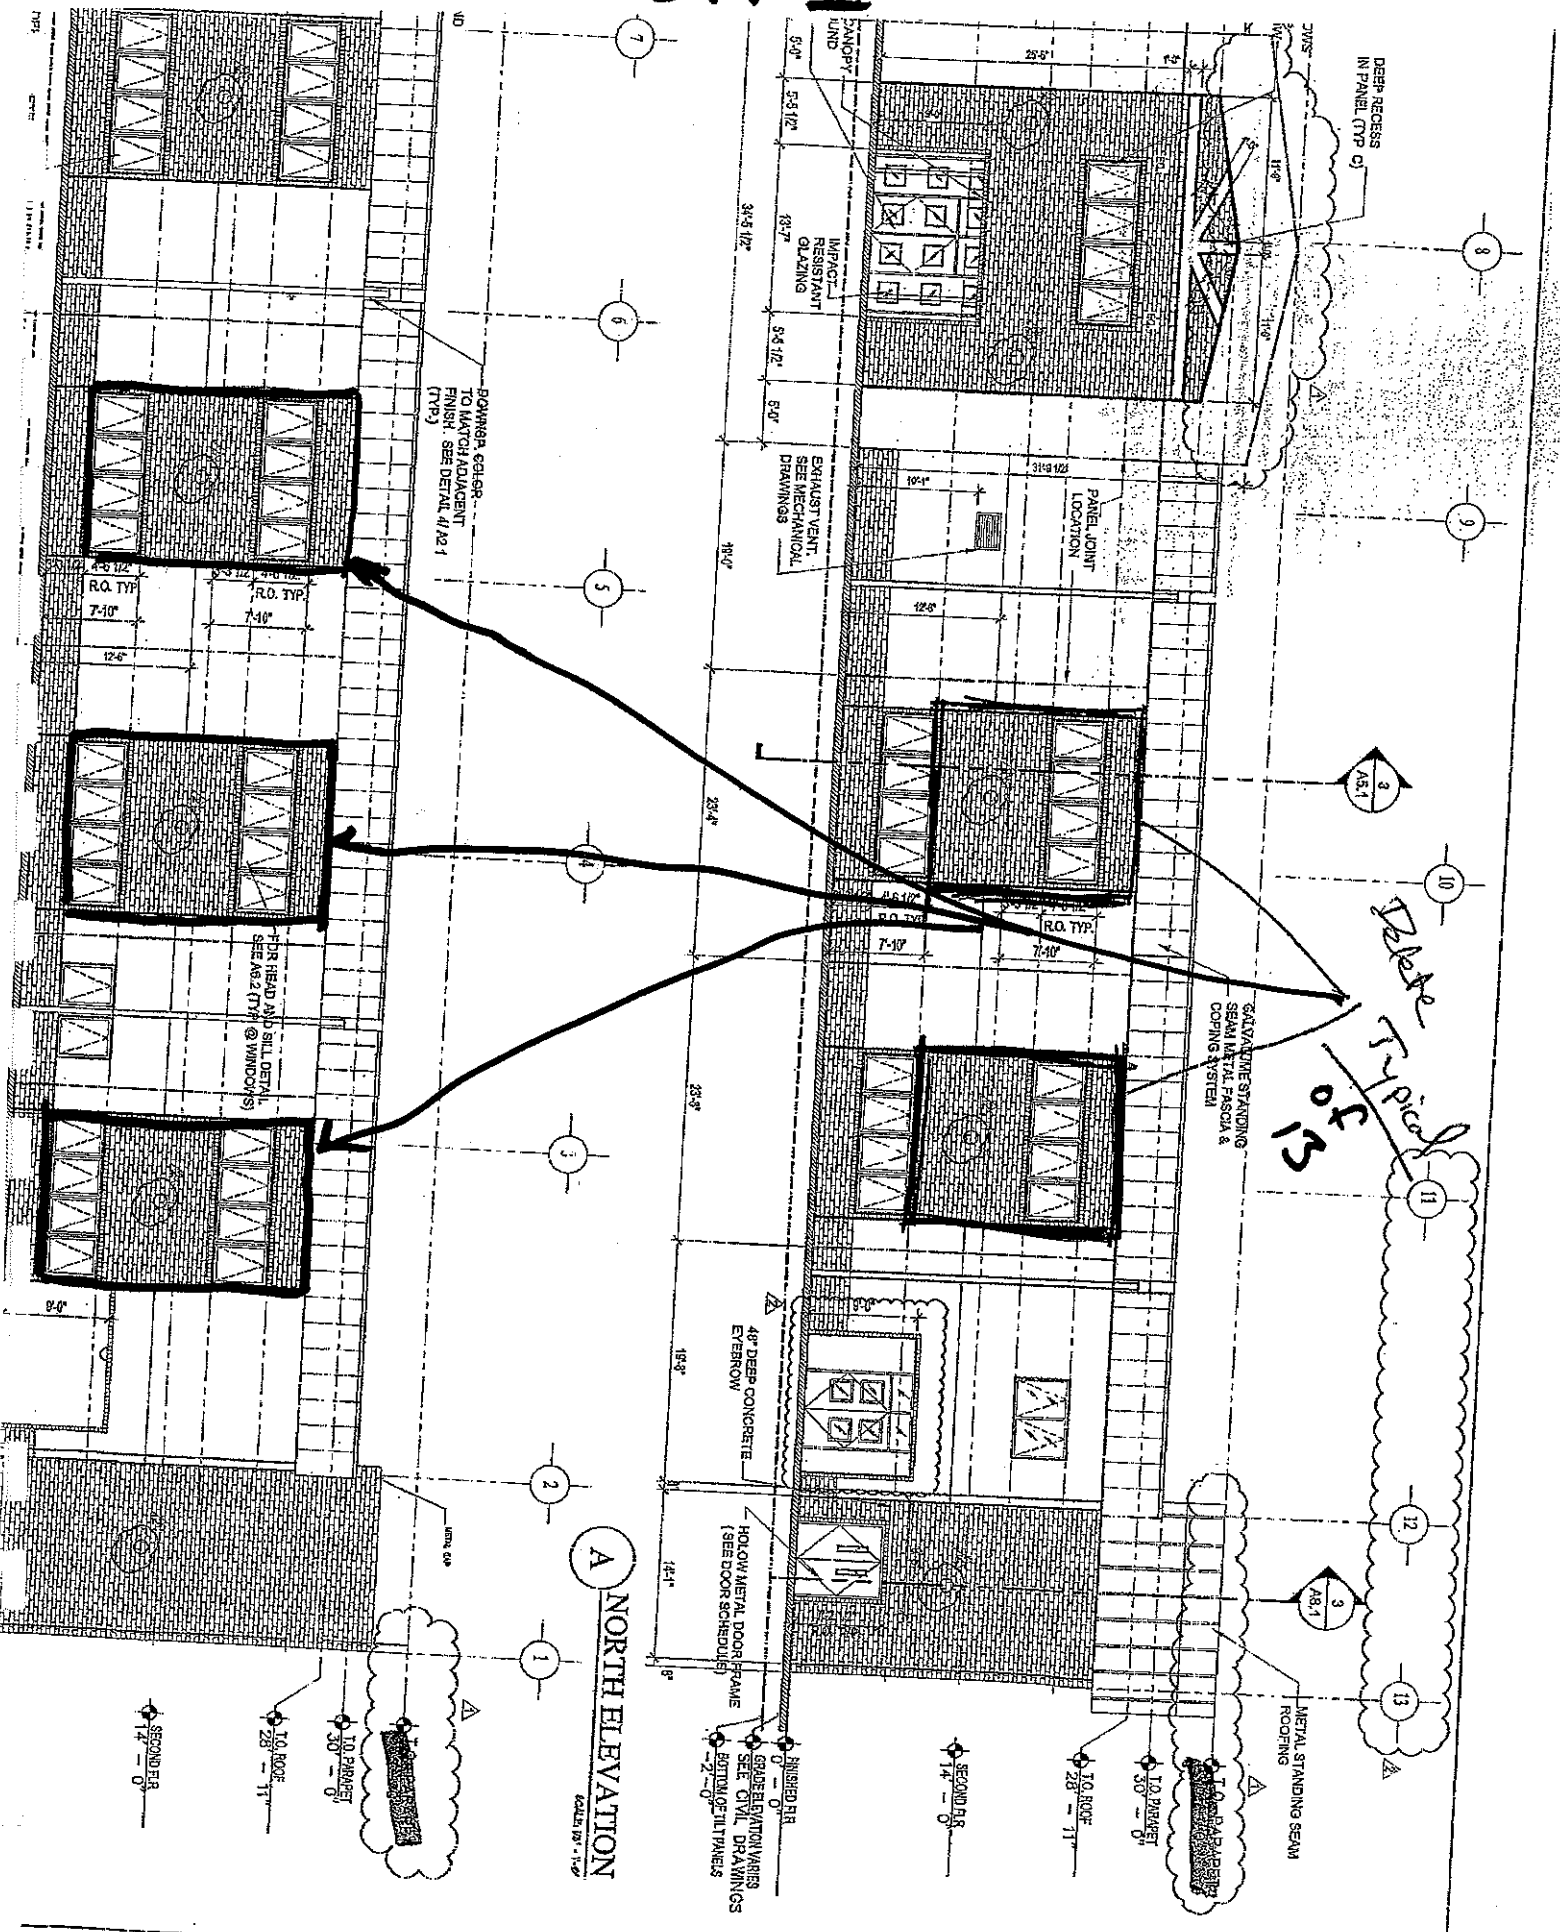


TAB 6

**EXHIBIT B  
GUARANTEED MAXIMUM PRICE SUMMARY**

**PROJECT NAME: Okeeheelee Middle School Classroom Addition  
PROJECT NO: 2151 - 8307**

DIVISION 1 - GENERAL REQUIREMENTS (Direct Cost Items Related to Site).....	\$	11,110
DIVISION 2 - SITE CONSTRUCTION.....	\$	636,505
DIVISION 3 - CONCRETE.....	\$	1,047,790
DIVISION 4 - MASONRY.....	\$	-
DIVISION 5 - STEEL.....	\$	538,980
DIVISION 6 - CARPENTRY.....	\$	270,741
DIVISION 7 - THERMAL/MOISTURE.....	\$	290,465
DIVISION 8 - WINDOWS AND DOORS.....	\$	273,690
DIVISION 9 - FINISHES.....	\$	655,805
DIVISION 10 - SPECIALTIES.....	\$	115,000
DIVISION 11 - EQUIPMENT.....	\$	3,900
DIVISION 12 - FURNISHINGS.....	\$	62,310
DIVISION 13 - SPECIAL CONSTRUCTION.....	\$	-
DIVISION 14 - ELEVATOR.....	\$	53,400
DIVISION 15 - MECHANICAL.....	\$	1,128,675
DIVISION 16 - ELECTRICAL.....	\$	949,000
TOTAL (divisions 1-16 including accepted value engineered items).....	\$	6,037,371
BONDS AND INSURANCE.....	\$	66,026
CONSTRUCTION PHASE FEE (On Site Staff).....	\$	592,821
GENERAL CONDITIONS (Direct Cost Items Related to Field Staff).....	\$	253,351
CONSTRUCTION MANAGER FEE (Overhead & Profit).....	\$	378,595
CONSTRUCTION CONTINGENCY.....	\$	180,788
ALLOWANCE (Extraordinary Costs).....	\$	-
DEDUCT : SALES TAX RECOVERY (Guaranteed).....	\$	(60,263)
TOTAL GUARANTEED MAXIMUM PRICE.....	\$	7,448,689
PRECONSTRUCTION PHASE FEE.....	\$	56,062
CCD No. 1.....	\$	57,111
TOTAL CONSTRUCTION COST (Preconstruction Fee + GMP).....	\$	7,561,862

Certified True and Correct by:


President
2/1/2007  
NAME/TITLE
DATE

**EXHIBIT C**  
**SUMMARY OF PRECONSTRUCTION FEE**

PROJECT NAME OKEEHOLEE MIDDLE SCHOOL ADDITION  
 PROJECT NO. 2151-8307  
 KAUFMAN LYNN INC., GENERAL CONTRACTORS, CGC 021732  
 Date: May 9, 2006

<u>Description of Service</u>	<u>Name/Title</u>	<u>Duration (weeks)</u>	<u>Hours / Wk</u>	<u>Rate / Hr</u>	<u>Total</u>
PMIS Reporting	Senior Project Executive	25.98	0.75	119.43	\$2,327.00
Schedule Control	Senior Project Executive	25.98	0.75	119.43	\$2,327.00
Subsystem/Master Project	Project Manager	25.98	0.25	78.65	\$510.83
Schedule	Project Manager	25.98	0.5	78.65	\$1,021.65
	Asst Pm (WMBE-CM)	25.98	0.4	78.65	\$817.32
	Superintendant	25.98	0.25	89.41	\$580.73
Project Accounting System	Project Corrdinator	25.98	0.5	45.53	\$591.48
Project Manual	Project Manager	25.98	0.75	78.65	\$1,532.48
	Asst Pm (WMBE-CM)	25.98	0.75	78.65	\$1,532.48
Cost Control (Design Review & Estimate):					
-Advanced Schematic	Preconstruction Manager	1.00	35	110.36	\$3,862.50
-Design Development	Preconstruction Manager	25.98	1	110.36	\$2,867.07
-50% CD	<b>Not Required - Per Owner</b>	0.00	0	0.00	\$0.00
-Solicitation of Bids / Establish GMP	Preconstruction Manager	4.25	10	110.36	\$4,690.17
	Senior Estimator	4.00	22	78.65	\$6,921.11
	Project Manager	4.25	15	78.65	\$5,013.87
	Asst Pm (WMBE-CM)	2.50	18	78.65	\$3,539.21
	Estimating Coordinator	3.00	16	24.01	\$1,152.42
<b>SUBTOTAL</b>					<b>\$39,287.30</b>

**Description**

Reimbursable Expenses	Plan Reproduction (Budget Reveivs)			4,270.00	\$4,270.00
	Budget Presentation Booklets			700.00	\$700.00
	Plan Reproduction (Bid Process)	115	87	10,005.00	\$10,005.00
	Plans Pack & Ship Expences	45	20	900.00	\$900.00
	Gas & Tolls Meetings / Site Visits	12	75	900.00	\$900.00
<b>SUBTOTAL</b>					<b>\$16,775.00</b>

**TOTAL PRECONSTRUCTION FEE** **\$56,062.30**

WMBE Cost on Labor = 15% **\$5,889.00**  
 Labor Rates Include (Labor, Insurance, Tax & General Liability)







**EXHIBIT F  
CONSTRUCTION TEAM ASSIGNED REPRESENTATIVES**

**PROJECT NAME: Okeeheelee Middle School Classroom Addition  
PROJECT NO: 2151 - 8307**

**Owner: School District of Palm Beach County**

**Owner's Authorized Representative: James Cartmill, Sr. Projects Administrator**

**Construction Manager: Kaufman Lynn, Inc. General Contractors CGC 021732**

**Architect Engineer: ACAI Associates, Inc.**

EXHIBIT I

Builder's Risk Questionnaire

Owner: School District of Palm Beach County, Florida

Contractor Name & Address: Kaufman Lynn, Inc. General Contractors, 622 Banyan Trail, Suite 300, Boca Raton, FL 33431

Project Title, Project Number & Description: Okeeheelee Middle School Classroom Addition, 2151-8307, Construction of new two-story classroom building addition

Project Address: 2200 Pinehurst Drive, Greenacres, FL 33413

Estimated Cost of Construction: New- \$ 7,448,689 Modernization- N / A

Intended use of Completed Structure: Classrooms

Number of Stories: 2 Number of Buildings: 1

Total GSF of Construction: 40,689

Construction Commencement: March 2007 Construction Completion: March 2008

Type of Construction: Walls- Tilt-Up Concrete Roof: Steel Bar Joist and Metal Deck

Footings on Fill, Ground, Piles or Other: Footing on Fill

Foundation Materials: Concrete

Distance to Nearest Fire Hydrant: 25 feet

Distance to Fire Department: 4 miles

Distance to Nearest Structure: 25 feet

Will Sprinklers Be Installed: Yes

Site Security (Fencing, Lighting, Security Service): Fencing with locked gates, Existing School's Locked Gates & Lights

Material Storage On-Site-

How Will Material Be Stored: Trailers & Containers Value: N / A

Will Flammables Be Stored On-Site & How: N / A

List the Major Subcontractors and Estimated Percent of Work: List Attached

Is Demolition Rquired (Describe:): Demolition of existing sidewalks and utilities for new building location

Completed By: R. Murrell Perry Date: February 1, 2007

**EXHIBIT S**  
**SUBCONTRACTORS PARTICIPATION**  
**DIVISIONS 1 - 16**

**PROJECT NAME:** Okeehelée Middle School Classroom Addition  
**PROJECT NO:** 2151 - 8307  
**APPROVED GMP AMOUNT:** \$ 7,448,689

Subject to Agreement with the Construction Manager, the Subcontractor firms listed below will participate in this project for the Contract (Trade) Items and the dollar amounts shown.

ITEM #	DESCRIPTION	COST (ACTUAL)	BUDGET (EST. COST)	SUBCONTRACTOR NAME	M/WBE (YES OR NO)	\$ AMOUNT	%
2	Demolition			DH Griffin	No		
2	Surveying			Brown & Phillips	Yes	\$ 14,295	0.19%
2	Sitework			Hughes Construction	No		
2	Flatwork			Cobra Construction	No		
2	Fencing			Tropic Fence	Yes	\$ 36,300	0.49%
2	Landscaping			Landscape Svc Pro.	Yes	\$ 55,935	0.75%
2	Irrigation			IRF	No		
3	Tilt-Up Concrete			Drawdy Brothers	No		
5	Structural Steel			Industrial Steel Fab	Yes	\$ 457,950	6.15%
6	Cabinetry			Institutional Products	No		
7	Waterproofing & Caulking			Coman	No		
7	Roofing Membrane			Triple M	No		
7	Lightweight Concrete			Don Works	No		
7	Metal Roofing			Aelcor	No		
8	Doors, Frames, Hardware			Arc One	No		
8	Door Installation			HRC	Yes	\$ 12,550	0.17%
8	Windows & Glass & Glazing			Sol-A-Trol	Yes	\$ 146,635	1.97%

Subcontractors represented as M/WBE Certified are according to requirements established in the Proposal Documents. Attach a copy of the Certification for each Subcontractor listed.

Contractor's Firm Name: Kaufman Lynn, Inc. General Contractors Total M/WBE Subcontractor Participation: \_\_\_\_\_

Name and Position (type or print): R. Murrell Perry, Vice President Percentage of Total Bid (Base & Alternates) \_\_\_\_\_

SIGNATURE: \_\_\_\_\_ Date: 1/3/2007

**EXHIBIT S  
SUBCONTRACTORS PARTICIPATION  
DIVISIONS 1 - 16**

**PROJECT NAME:** Okeeheltee Middle School Classroom Addition  
**PROJECT NO:** 2151 - 8307  
**APPROVED GMP AMOUNT:** \$ 7,448,689

Subject to Agreement with the Construction Manager, the Subcontractor firms listed below will participate in this project for the Contract (Trade) items and the dollar amounts shown.

ITEM #	DESCRIPTION	COST (ACTUAL)	BUDGET (EST. COST)	SUBCONTRACTOR NAME	M/WBE (YES OR NO)	\$ AMOUNT	%
9	Drywall & Metal Framing			Atlantic Interiors	Yes	\$ 363,120	4.87%
9	Stucco & Exterior Framing			SPD	No		
9	Tile Flooring			Pallais	Yes	\$ 59,870	0.80%
9	Acoustical Ceilings			Superior Interiors	Yes	\$ 58,430	0.78%
9	VCT Flooring			Brookside	No		
9	Painting			Gray's Painting	No		
10	Visual Display Boards			Florida Chalkboard	No		
10	Louvers			GC Building Products	No		
10	Aluminum Walkway Canopy			Walker Design	No		
10	Fire Extinguishers			Triangle Fire	No		
10	Bathroom Accessories			Elechs	No		
10	Metal Shelving			List Industries	No		
10	Signage			Full Moon Over Florida	Yes	\$ 12,290	0.16%
12	Chemistry Casework			Newton	No		
12	Window Treatments			Nat'l Stage & Window	No		
14	Elevators			ThyssenKrupp	No		
15	Fire Sprinklers			Farmer & Irwin	No		

Subcontractors represented as M/WBE: Certified are according to requirements established in the Proposal Documents. Attach a copy of the Certification for each Subcontractor listed.

Contractor's Firm Name: Kaufman Lynn, Inc. General Contractors Total M/WBE Subcontractor Participation: \_\_\_\_\_

Name and Position (type or print): R. Murrell Perry, Vice President Percentage of Total Bid (Base & Alternates) \_\_\_\_\_

SIGNATURE: \_\_\_\_\_ Date: 1/3/2007



**EXHIBIT S  
LIST OF MAJOR SUBCONTRACTORS**

**PROJECT NAME: Okeehelée Middle School Classroom Addition  
PROJECT NO: 2151 - 8307**

<b>Division of Work</b>	<b>Corporate Name and Address</b>	<b>Principal or Officer's Name</b>	<b>License Number</b>
<b>Fire Sprinkler</b>	<b>Farmer &amp; Irwin Corp. 3300 Avenue K Riviera Beach, FL 33419</b>	<b>Steven Irwin</b>	<b>06253800011997</b>
<b>Electrical</b>	<b>Fastrac Electric Corp. 810 Saturn Street Suite #25 Jupiter, FL 33477</b>	<b>Shawn Bly</b>	<b>EC0002876</b>
<b>Plumbing</b>	<b>Farmer &amp; Irwin Corp. 3300 Avenue K Riviera Beach, FL 33419</b>	<b>Steven Irwin</b>	<b>CFC020327</b>
<b>Mechanical</b>	<b>Farmer &amp; Irwin Corp. 3300 Avenue K Riviera Beach, FL 33419</b>	<b>Steven Irwin</b>	<b>CMC1249623</b>
<b>Roofing</b>	<b>Triple M Roofing Corp. 914 NW 19th Avenue Fort Lauderdale, FL 33311</b>	<b>Richard Milanese</b>	<b>CCC1326182</b>
<b>Concrete</b>	<b>Drawdy Brothers Construction II, Inc. 2945 W. Midway Road Ft. Pierce, FL 34981</b>	<b>Troy Drawdy</b>	<b>CGCA13797</b>
<b>Structural</b>	<b>Industrial Steel Fab. Inc. 11518 Normandy Blvd Jacksonville, FL 32236</b>	<b>Minnie Pllum</b>	<b>CGC053643</b>
<b>Sitework</b>	<b>Hughes Construction 3101 Fairlane Farms Road #1 Wellington, FL 33414</b>	<b>Todd Hughes</b>	<b>CUC052600</b>

TAB 7





January 23, 2004

Certification Date: 1/23/2004 - 1/23/2007

Office of  
Small Business Assistance

50 S Military Trail, Suite 209

West Palm Beach, FL 33415

(561) 616-6840

Fax: (561) 616-6860

www.pbcgov.com

SERVICES: Surveying Services  
Mapping

Brown & Phillips, Inc.  
3969 Haverhill Road, Suite 105  
West Palm Beach, FL 33417

Attention: Anthony Brown

Palm Beach County  
Board of County  
Commissioners

Warren H. Newell, Chairman

Carol A. Roberts, Vice Chair

Karen T. Marcus

Mary McCarty

Burt Aaronson

Tony Masilotti

Addie I. Greene

County Administrator

Robert Weisman

The Palm Beach County Office of Small Business Assistance has completed its review of the documents you submitted for renewal of your firm's certification and is pleased to announce that your firm has been certified as a Small/Minority Business Enterprise (S/MBE) for three (3) years.

Your firm shall be subject to the provisions of the Palm Beach County Purchasing Ordinance and all State and Federal laws relating to the transaction of business.

This certification entitles you to participate in contracting opportunities when the products and services offered by your firm are being considered for bid. As an additional service to your firm, you will be included in the Palm Beach County Directory of certified SBE firms. If you wish to have your firm's listing changed, please contact our office at (561) 616-6840.

Your company's certification is subject to periodic review to verify your continued eligibility. You are required to notify us if at any time the minority status of your firm changes. Failure to report changes in the status of your firm may result in your firm being decertified.

Sincerely,

Vicki Hobbs  
Certification Technician

"An Equal Opportunity

Affirmative Action Employer"



The School District of Palm Beach County, FL  
3300 Forest Hill Blvd., Suite A-106  
West Palm Beach, FL 33406-5813

Office of Diversity In Business Practices

Arthur C. Johnson Ph.D., Superintendent  
Lois Salton, Specialist  
Telephone: (561) 434-8532  
Fax: (561) 434-7405  
Bid Hotline: (561) 434-8111  
E-Mail: salton@palmbeach.k12.fl.us

# Congratulations!

APR 19 2004

The School District of Palm Beach County has certified your firm **TROPIC FENCE, INC.** as a Minority/Woman Business Enterprise (M/WBE). Your certification is valid for three years, from: April 15, 2004 - July 01, 2007.

Certification is not a guarantee that your firm will receive work. If you do not have a vendor number, you will be issued with one. Our bid hotline is a valuable source of information.

You must notify this office if the status of your firm changes. Failure to report changes that affect the ownership and control of your firm may result in decertification.

It is the vendor's responsibility to maintain the certification. If the certification expires, a contract may be terminated and awarded to another vendor.

Your certification is not a blanket conveyance. You have requested certification, demonstrated managerial control or ability, or hold license in a specific trade, commodity or discipline. This certification letter identifies the areas in which your firm has been certified: **FENCE INSIALLATION AND REPAIR.** While you may bid on any service or commodity that you feel qualified for, this certification and any benefits to be derived (preferences or other considerations) shall only be attributable to the trade, service or commodity indicated on the certification letter. Please examine this certificate letter and advise us of any concerns. Any change to your certification requires you to submit proof of expertise, licensure and a business history (at minimum) to justify the additional certification. You are also required to submit a copy of your certification letter with each bid, or proposal that you submit to the School District.

This congratulations certification letter lists those areas for which your firm has been certified. The benefits afforded a certified M/WBE will apply only to those areas listed on the certificate. For this reason, we suggest that you keep us advised of all changes relevant to your certification. Again, you must submit a copy of your certification letter with each bid or proposal you submit to the School District.

Sincerely,

*Lois Salton*

Lois Salton  
Specialist

*"An Equal Opportunity Employer"*



The School District of Palm Beach County, FL  
3300 Forest Hill Blvd., Suite A-106  
West Palm Beach, FL 33406-5813

Office of Diversity In Business Practices

Arthur C. Johnson Ph.D., Superintendent  
Pamela Morgan, Analyst  
Telephone: (561) 434-7422  
Fax: (561) 434-7405  
Bid Hotline: (561) 434-8111  
E-Mail: morganp@palmbeach.k12.fl.us

# Congratulations!

The School District of Palm Beach County has certified your firm: Landscape Service Professionals, as a Minority/Woman Business Enterprise (M/WBE). Your certification is valid for three years, from: December 31, 2004 - December 31, 2007.

Certification is not a guarantee that your firm will receive work. If you do not have a vendor number, you will be issued with one. Our bid hotline is a valuable source of information.

You must notify this office if the status of your firm changes. Failure to report changes that affect the ownership and control of your firm may result in decertification.

It is the vendor's responsibility to maintain the certification. If the certification expires, a contract may be terminated and awarded to another vendor.

Your certification is **not a blanket conveyance**. You have requested certification, demonstrated managerial control or ability, or hold license in a specific trade, commodity or discipline. This certification letter identifies the areas in which your firm has been certified: LANDSCAPE, IRRIGATION, TREE RELOCATION. While you may bid on any service or commodity that you feel qualified for, this certification and any benefits to be derived (preferences or other considerations) shall only be attributable to the trade, service or commodity indicated on the certification letter. Please examine this certificate letter and advise us of any concerns. Any change to your certification requires you to submit proof of expertise, licensure and a business history (at minimum) to justify the additional certification. You are also required to submit a copy of your certification letter with each bid, or proposal that you submit to the School District.

This congratulations certification letter lists those areas for which your firm has been certified. The benefits afforded a certified M/WBE will apply only to those areas listed on the certificate. For this reason, we suggest that you keep us advised of all changes relevant to your certification. Again, you **must** submit a copy of your certification letter with each bid or proposal you submit to the School District.


Sincerely,

*Pamela Morgan*

Pamela Morgan  
Analyst

*"An Equal Opportunity Employer"*


*Florida Statewide  
Inter-Local Certification*



Florida Department of Management Services  
Office of Supplier Diversity

**INDUSTRIAL STEEL FABRICATORS INC.**

is certified as a **Minority Business Enterprise**  
under the provisions of Chapter 287, Florida Statutes and Inter-Local Agreement,  
for a one-year period from August 9, 2006 to August 9, 2007

  
Director



The School District of Palm Beach County, FL  
3300 Forest Hill Blvd., Suite A-106  
West Palm Beach, FL 33406-5813

Office of Diversity In Business Practices

Arthur C. Johnson Ph.D., Superintendent  
Pamela Morgan, Analyst  
Telephone: (561) 434-7422  
Fax: (561) 434-7405  
Bid Hotline: (561) 434-8111  
E-Mail: morganp@palmbeach.k12.fl.us

# Congratulations!

The School District of Palm Beach County has certified your firm HURRICANE RESISTANT CONSTRUCTION INC as a Minority/Woman Business Enterprise (M/WBE). Your certification is valid for three years, from JANUARY 1, 2006 - JANUARY 01, 2009. Certification is not a guarantee that your firm will receive work. If you do not have a vendor number, you will be issued with one. Our bid hotline is a valuable source of information.

You must notify this office if the status of your firm changes. Failure to report changes that affect the ownership and control of your firm may result in decertification.

It is the vendor's responsibility to maintain the certification. If the certification expires, a contract may be terminated and awarded to another vendor.

Your certification is not a blanket conveyance. You have requested certification, demonstrated managerial control or ability, or hold license in a specific trade, commodity or discipline. This certification letter identifies the areas in which your firm has been certified HOLLOW METAL FRAMES IN MASONRY; METAL AND WOOD DOORS; ARCHITECTURAL HARDWARE SERVICES. While you may bid on any service or commodity that you feel qualified for, this certification and any benefits to be derived (preferences or other considerations) shall only be attributable to the trade, service or commodity indicated on the certification letter. Please examine this certificate letter and advise us of any concerns. Any change to your certification requires you to submit proof of expertise, licensure and a business history (at minimum) to justify the additional certification. You are also required to submit a copy of your certification letter with each bid, or proposal that you submit to the School District.

This congratulations certification letter lists those areas for which your firm has been certified. The benefits afforded a certified M/WBE will apply only to those areas listed on the certificate. For this reason, we suggest that you keep us advised of all changes relevant to your certification. Again, you must submit a copy of your certification letter with each bid or proposal you submit to the School District.

Sincerely,

*Pamela Morgan*

Pamela Morgan  
Analyst

*"An Equal Opportunity Employer"*

FROM : SOL-A-TROL



The School District of Palm Beach County, FL  
3300 Forest Hill Blvd., Suite A-106  
West Palm Beach, FL 33408-5813

Office of Diversity In Business Practices

Arthur C. Johnson Ph.D., Superintendent  
Pamela Morgan, Analyst  
Telephone: (561) 434-7422  
Fax: (561) 434-7405  
Bid Hotline: (561) 434-8111  
E-Mail: morgaup@palmbeach.k12.fl.us

# Congratulations!

The School District of Palm Beach County has certified your firm: SOL-A-TROL, as a Minority/Woman Business Enterprise (M/WBE). Your certification is valid for three years, from: MAY 2, 2004 - MAY 2, 2007.

Certification is not a guarantee that your firm will receive work. If you do not have a vendor number, you will be issued with one. Our bid hotline is a valuable source of information.

You must notify this office if the status of your firm changes. Failure to report changes that affect the ownership and control of your firm may result in decertification.

It is the vendor's responsibility to maintain the certification. If the certification expires, a contract may be terminated and awarded to another vendor.

Your certification is not a blanket conveyance. You have requested certification, demonstrated managerial control or ability, or hold license in a specific trade, commodity or discipline. This certification letter identifies the areas in which your firm has been certified: ALUMINUM WINDOW MANUFACTURING. While you may bid on any service or commodity that you feel qualified for, this certification and any benefits to be derived (preferences or other considerations) shall only be attributable to the trade, service or commodity indicated on the certification letter. Please examine this certificate letter and advise us of any concerns. Any change to your certification requires you to submit proof of expertise, licensure and a business history (at minimum) to justify the additional certification. You are also required to submit a copy of your certification letter with each bid, or proposal that you submit to the School District.

This congratulations certification letter lists those areas for which your firm has been certified. The benefits afforded a certified M/WBE will apply only to those areas listed on the certificate. For this reason, we suggest that you keep us advised of all changes relevant to your certification. Again, you must submit a copy of your certification letter with each bid or proposal you submit to the School District.

Sincerely,

*Pamela Morgan*

Pamela Morgan  
Analyst

€

"An Equal Opportunity Employer"

MAY 18 2004



The School District of Palm Beach County, FL  
3300 Forest Hill Blvd., Suite A-106  
West Palm Beach, FL 33406-5813

Office of Diversity In Business Practices

Arlene C. Johnson Ph.D., Superintendent  
Pamela Morgan, Analyst  
Telephone: (561) 434-7422  
Fax: (561) 434-7405  
Bid Hotline: (561) 434-8111  
E-Mail: [morganp@palmbeach.k12.fl.us](mailto:morganp@palmbeach.k12.fl.us)

# Congratulations!

The School District of Palm Beach County has certified your firm Atlantic Interior Contracting, Inc., as a Minority/Woman Business Enterprise (M/WBE). Your certification is valid for three years, from JUNE 30, 2005 - JUNE 30, 2008.

Certification is not a guarantee that your firm will receive work. If you do not have a vendor number, you will be issued with one. Our bid hotline is a valuable source of information.

You must notify this office if the status of your firm changes. Failure to report changes that affect the ownership and control of your firm may result in decertification.

It is the vendor's responsibility to maintain the certification. If the certification expires, a contract may be terminated and awarded to another vendor.

Your certification is not a blanket conveyance. You have requested certification, demonstrated managerial control or ability, or hold license in a specific trade, commodity or discipline. This certification letter identifies the areas in which your firm has been certified in General Contractor, Drywall and Acoustical Ceiling. While you may bid on any service or commodity that you feel qualified for, this certification and any benefits to be derived (preferences or other considerations) shall only be attributable to the trade, service or commodity indicated on the certification letter. Please examine this certificate letter and advise us of any concerns. Any change to your certification requires you to submit proof of expertise, licensure and a business history (at minimum) to justify the additional certification. You are also required to submit a copy of your certification letter with each bid, or proposal that you submit to the School District.

This congratulations certification letter lists those areas for which your firm has been certified. The benefits afforded a certified M/WBE will apply only to those areas listed on the certificate. For this reason, we suggest that you keep us advised of all changes relevant to your certification. Again, you must submit a copy of your certification letter with each bid or proposal you submit to the School District.

Sincerely,

*Pamela Morgan*

Pamela Morgan  
Analyst

*"An Equal Opportunity Employer"*





The School District of Palm Beach County, FL  
3300 Forest Hill Blvd., Suite A-106  
West Palm Beach, FL 33406-5813

Office of Diversity In Business Practices

Arthur C. Johnson Ph.D., Superintendent  
Pamela Morgan, Analyst  
Telephone: (561) 434-7422  
Fax: (561) 434-7405  
Bid Hotline: (561) 434-8111  
E-Mail: morgaup@palmbeach.k12.fl.us

# Congratulations!

The School District of Palm Beach County has certified your firm Superior Interior Systems Inc. as a Minority/Woman Business Enterprise (M/WBE). Your certification is valid for three years, from JUNE 30, 2005 - JUNE 30, 2008.

Certification is not a guarantee that your firm will receive work. If you do not have a vendor number, you will be issued with one. Our bid hotline is a valuable source of information.

You must notify this office if the status of your firm changes. Failure to report changes that affect the ownership and control of your firm may result in decertification.

It is the vendor's responsibility to maintain the certification. If the certification expires, a contract may be terminated and awarded to another vendor.

Your certification is not a blanket conveyance. You have requested certification, demonstrated managerial control or ability, or hold license in a specific trade, commodity or discipline. This certification letter identifies the areas in which your firm has been certified in Installation of Acoustical Ceilings. While you may bid on any service or commodity that you feel qualified for, this certification and any benefits to be derived (preferences or other considerations) shall only be attributable to the trade, service or commodity indicated on the certification letter. Please examine this certificate letter and advise us of any concerns. Any change to your certification requires you to submit proof of expertise, licensure and a business history (at minimum) to justify the additional certification. You are also required to submit a copy of your certification letter with each bid, or proposal that you submit to the School District.

This congratulations certification letter lists those areas for which your firm has been certified. The benefits afforded a certified M/WBE will apply only to those areas listed on the certificate. For this reason, we suggest that you keep us advised of all changes relevant to your certification. Again, you must submit a copy of your certification letter with each bid or proposal you submit to the School District.

Sincerely,

*Pamela Morgan*

Pamela Morgan  
Analyst

*"An Equal Opportunity Employer"*





The School District of Palm Beach County, FL  
3300 Forest Hill Blvd., Suite A-108  
West Palm Beach, FL 33406-5813

Office of Diversity In Business Practices

Arthur C. Johnson Ph.D., Superintendent  
Pamela Morgan, Analyst  
Telephone: (561) 434-7422  
Fax: (561) 434-7408  
Bid Hotline: (561) 434-8111  
E-Mail: morganp@palmbeach.k12.fl.us

# Congratulations!

The School District of Palm Beach County has certified Full Moon Over Florida Inc as a Minority/Woman Business Enterprise (M/WBE). Your certification is valid for three years, from August 22, 2006 - August 22, 2009.

Certification is not a guarantee that your firm will receive work. If you do not have a vendor number, you will be issued with one. Our bid hotline is a valuable source of information.

You must notify this office if the status of your firm changes. Failure to report changes that affect the ownership and control of your firm may result in decertification.

It is the vendor's responsibility to maintain the certification. If the certification expires, a contract may be terminated and awarded to another vendor.

Your certification is not a blanket conveyance. You have requested certification, demonstrated managerial control or ability, or hold license in a specific trade, commodity or discipline. This certification letter identifies the areas in which your firm has been Signs, Building Plaques and Interior Signage any benefits to be derived (preferences or other considerations) shall only be attributable to the trade, service or commodity indicated on the certification letter. Please examine this certificate letter and advise us of any concerns. Any change to your certification requires you to submit proof of expertise, licensure and a business history (at minimum) to justify the additional certification. You are also required to submit a copy of your certification letter with each bid, or proposal that you submit to the School District.

This congratulations certification letter lists those areas for which your firm has been certified. The benefits afforded a certified M/WBE will apply only to those areas listed on the certificate. For this reason, we suggest that you keep us advised of all changes relevant to your certification. Again, you must submit a copy of your certification letter with each bid or proposal you submit to the School District.

Sincerely,

*Pamela Morgan*

Pamela Morgan  
Analyst

*"An Equal Opportunity Employer"*

TAB 8



STATE OF FLORIDA

DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION

CONSTRUCTION INDUSTRY LICENSING BOARD  
1940 NORTH MONROE STREET  
TALLAHASSEE FL 32399-0783

(850) 487-1395

LEWIS, RUFFER LEE JR  
D H GRIFFIN WRECKING COMPANY INC  
PO BOX 7267  
PENSACOLA FL 32534

STATE OF FLORIDA AC# 2751281

DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION

CGC1508294 08/25/06 068037699

CERTIFIED GENERAL CONTRACTOR  
LEWIS, RUFFER LEE JR  
D H GRIFFIN WRECKING COMPANY INC

IS CERTIFIED under the provisions of Ch. 489 FS.  
Expiration date: AUG 31, 2008 068037699

DETACH HERE

AC# 2751281

STATE OF FLORIDA

DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION  
CONSTRUCTION INDUSTRY LICENSING BOARD SEQ#L06082502285

DATE	BATCH NUMBER	LICENSE NBR
08/25/2006	068037699	CGC1508294

The GENERAL CONTRACTOR  
Named below IS CERTIFIED  
Under the provisions of Chapter 489 FS.  
Expiration date: AUG 31, 2008

LEWIS, RUFFER LEE JR  
D H GRIFFIN WRECKING COMPANY INC  
1312 WEST NINE MILE ROAD  
PENSACOLA FL 32534

JEB BUSH GOVERNOR

SIMONE MARSTILLER SECRETARY

DISPLAY AS REQUIRED BY LAW

2005-04530

STATE OF FLORIDA  
PALM BEACH COUNTY  
OCCUPATIONAL LICENSE

05-032  
CLASSIFICATION

**EXPIRES: SEPTEMBER - 30 - 2007**

BROWN & PHILLIPS INC  
PHILLIPS III JOHN E &  
BROWN ANTHONY ST CLAIR

\*\* LOCATED AT  
901 NORTHPOINT PARKWAY #305  
WEST PALM BEACH FL 33407

CNTY \$33.00

TOTAL \$33.00

Is hereby licensed at above address for the period beginning on the first day of October and ending on the thirtieth day of September to engage in the business, profession or occupation of:

LAND SURVEYOR & MAPPER  
LB0006473  
LS0004826/LS0004977

**THIS IS NOT A BILL - DO NOT PAY**

PAID. PBC TAX COLLECTOR  
\$33.00 OCC 049 041806 09-11-2006

Peter H. Carney  
TAX COLLECTOR, PALM BEACH COUNTY

**THIS LICENSE VALID ONLY WHEN RECEIPTED BY  
TAX COLLECTOR**

#1888422

STATE OF FLORIDA


DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION  
BOARD OF PROF. SURVEYORS & MAPPERS

SEQ#L05030200930

DATE	BATCH NUMBER	LICENSE NBR
3/02/2005	040723286	LB6473

The SURVEYING & MAPPING BUSINESS  
Named below IS CERTIFIED  
Under the provisions of Chapter 472, FS.  
Expiration date: FEB 28, 2007

BROWN & PHILLIPS INC  
901 NORTHPOINT PARKWAY  
SUITE 305  
WEST PALM BEACH FL 33407



JEB BUSH  
GOVERNOR

DIANE CARR  
SECRETARY

DISPLAY AS REQUIRED BY LAW

#1888386

STATE OF FLORIDA


DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION  
BOARD OF PROF. SURVEYORS & MAPPERS

SEQ#L05030200894

DATE	BATCH NUMBER	LICENSE NBR
3/02/2005	040719019	LS4826

The SURVEYOR AND MAPPER  
Named below IS LICENSED  
Under the provisions of Chapter 472, FS.  
Expiration date: FEB 28, 2007

PHILLIPS, JOHN E III  
6699 WILSON ROAD  
WEST PALM BEACH FL 33413



JEB BUSH  
GOVERNOR

DIANE CARR  
SECRETARY

DISPLAY AS REQUIRED BY LAW

#1888333

STATE OF FLORIDA

DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION  
BOARD OF PROF. SURVEYORS & MAPPERS

SEQ#L05030200841

DATE	BATCH NUMBER	LICENSE NBR
3/02/2005	040719243	LS4977

The SURVEYOR AND MAPPER  
Named below IS LICENSED  
Under the provisions of Chapter 472, FS.  
Expiration date: FEB 28, 2007

BROWN, ANTHONY ST  
4026 WAVERLY DRIVE  
WEST PALM BEACH FL 33407



CITY OF WEST PALM BEACH

DEPARTMENT OF CONSTRUCTION SERVICES



Dear Business Owner,

This is your Occupational License / Certificate of Use for the 2006-2007 business year. I appreciate your participation in the continued growth of the City of West Palm Beach. If we can be of assistance please do not hesitate to contact us by telephone or fax at the numbers shown below. Please read the instructions carefully regarding the posting of this Occupational License / Certificate of Use. Furthermore, please be advised that, pursuant to Section 22-39 of the City's Code of Ordinances, a Certificate of Use may be suspended or revoked upon certain violations of city, county or state law.

Sincerely,

Neil K. Melick, CBO  
BUILDING OFFICIAL

FOR INFORMATION CALL (561) 805-6700 OR FAX (561) 805-6676 / HOURS 8:00 AM - 5:00 PM — MONDAY - FRIDAY

INSTRUCTIONS: PLEASE DETACH BELOW ▼ AND POST IN A CONSPICUOUS PLACE AT YOUR PLACE OF BUSINESS.



CITY OF WEST PALM BEACH  
2006-07 LICENSE / CERTIFICATE OF USE

NOT TRANSFERABLE

CITY OF WEST PALM BEACH  
100 WEST PALM BEACH BLVD. 33411

LAND SURVEYING

0000013564-1  
BROWN & PHILLIPS INC  
901 NORTHPOINT PKWY # 305

LICENSE NO	CATEGORY	DESCRIPTION	FEE
35663	8714	SURVEYING SERVICES OFFICE ONLY	82.68
CHANGES	PENALTIES	TOTAL	
THIS DOCUMENT NOT VALID UNTIL FUNDS ARE COLLECTED		0.00	82.68
		** PAID	82.68
		** BAL **	0.00

EXPIRES  
SEPTEMBER 30,  
2007



STATE OF FLORIDA

DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION

CONSTRUCTION INDUSTRY LICENSING BOARD  
1940 NORTH MONROE STREET  
TALLAHASSEE FL 32399-0783

(850) 487-1395

HUGHES, TODD ALEXANDER  
HUGHES CONSTRUCTION INDUSTRIES INC  
3500 FAIRLANE FARMS RD #5  
WELLINGTON FL 33414

STATE OF FLORIDA AC# 2620252  
DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION

CUC052600 06/16/06 050821559

CERT UNDERGROUND & EXCAV ENTER  
HUGHES, TODD ALEXANDER  
HUGHES CONSTRUCTION INDUSTRIES IN

IS CERTIFIED under the provisions of Ch. 489 FS.  
Expiration date: AUG 31, 2008 L05061500783

DETACH HERE

AC# 2620252 STATE OF FLORIDA  
DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION  
CONSTRUCTION INDUSTRY LICENSING BOARD SEQ# L05061500783

DATE	BATCH NUMBER	LICENSE NBR
06/16/2006	050821559	CUC052600

The UNDERGROUND UTILITY & EXCAVATION CO  
Named below IS CERTIFIED  
Under the provisions of Chapter 489 FS.  
Expiration date: AUG 31, 2008

HUGHES, TODD ALEXANDER  
HUGHES CONSTRUCTION INDUSTRIES INC  
800 LAKE WELLINGTON DRIVE  
WEST PALM FL 33414

JEE BUSH GOVERNOR SIMONE MARSTILLER SECRETARY

DISPLAY AS REQUIRED BY LAW

Attn: Linda

AC# 2690596

STATE OF FLORIDA  
DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION  
CONSTRUCTION INDUSTRY LICENSING BOARD

SEQ# 106080101222

DATE	BATCH NUMBER	LICENSE NBR
08/01/2006	D5B018672	CGCD32699

The GENERAL CONTRACTOR  
Named below IS CERTIFIED  
Under the provisions of Chapter 489 FS.  
Expiration date: AUG 31, 2008

SPADA, RONALD MARTIN  
COBRA CONSTRUCTION CORPORATION  
735 SW 15TH AVE  
GULF STREAM, FL 33444

JEB BUSH  
GOVERNOR

SIMONE MARSTILLER  
SECRETARY

DISPLAY AS REQUIRED BY LAW



**PALM BEACH COUNTY CONTRACTORS  
CERTIFICATE OF COMPETENCY**

EXPIRES SEPTEMBER 30, 2007  
ADDRESS: 1864 NW 21ST STREET  
POMPANO BEACH, FL 33069  
IDENTIFICATION NUMBER: U-13588

NAME: STEVEN P. NESPOLI  
FIRM: TROPIC FENCE COMPANY

1864 NW 21ST ST  
POMPANO BEACH, FL 33069

1985-05832

STATE OF FLORIDA  
PALM BEACH COUNTY  
**OCCUPATIONAL LICENSE**

OC-032  
CLASSIFICATION

EXPIRES: SEPTEMBER - 30 - 2007

COUNTY

TROPIC FENCE COMPANY  
NESPOLI STEVE P

LOCATED AT  
1864 NW 21ST STREET  
POMPANO BEACH FL 33069-1306

CNTY \$27.50

TOTAL \$27.50

Is hereby licensed at above address for the period beginning on the first day of October and ending on the thirtieth day of September to engage in the business, profession or occupation of:  
FENCE CONTRACTOR  
U13588

**THIS IS NOT A BILL - DO NOT PAY**  
PAID: PBC TAX COLLECTOR  
\$27.50 OCC 049 034054 09-13-2006

Peter H. Carney  
TAX COLLECTOR - PALM BEACH COUNTY

**THIS LICENSE VALID ONLY WHEN RECEIPTED BY  
TAX COLLECTOR**

1991-06102

STATE OF FLORIDA  
PALM BEACH COUNTY  
**OCCUPATIONAL LICENSE**

CF-008  
CLASSIFICATION

EXPIRES: SEPTEMBER - 30 - 2007

COUNTY-WIDE

TROPIC FENCE COMPANY  
NESPOLI STEVE P

LOCATED AT  
1864 NW 21ST STREET  
POMPANO BEACH FL 33069-1306

C/WIDE \$185.85

TOTAL \$185.85

Is hereby licensed at above address for the period beginning on the first day of October and ending on the thirtieth day of September to engage in the business, profession or occupation of:  
FENCE ERECTION CONTRACTOR  
U13588

**THIS IS NOT A BILL - DO NOT PAY**  
PAID: PBC TAX COLLECTOR  
\$185.85 OCC 049 044055 09-13-2006

Peter H. Carney  
TAX COLLECTOR - PALM BEACH COUNTY

**THIS LICENSE VALID ONLY WHEN RECEIPTED BY  
TAX COLLECTOR**

2006-06443



STATE OF FLORIDA

PALM BEACH COUNTY

OCCUPATIONAL LICENSE

EXPIRES: SEPTEMBER - 30 - 2007

OS-012

CLASSIFICATION

LANDSCAPE SERVICE PROFESSIONAL  
INC  
WILSON SANDRA

\*\*\* LOCATED AT

6105 NW 77TH WAY  
TAMARAC FL 33321

CNTY \$33.00

TOTAL \$33.00

I am hereby licensed at above address for the period beginning on the  
first day of October and ending on the thirty first day of September to  
engage in the business, profession or occupation of

LANDSCAPING

THIS IS NOT A BILL - DO NOT PAY

PAY TO: PBC TAX COLLECTOR  
\$33.00 TCC 049 040661 09-08-2006

Peter H. Carney  
TAX COLLECTOR, PALM BEACH COUNTY

THIS LICENSE VALID ONLY WHEN RECEIPTED BY  
TAX COLLECTOR

# IMPORTANT!

## THIS IS YOUR CERTIFICATE OF COMPETENCY PALM BEACH COUNTY, FLORIDA

### PALM BEACH COUNTY CONTRACTORS CERTIFICATE OF COMPETENCY

EXPIRES SEPTEMBER 30, 20 07

AUDIT CONTROL NUMBER	A-0660941	CERTIFICATE NUMBER	U-20415
----------------------	-----------	--------------------	---------

**NAME FIRM** KALEEL UNIA COZER  
 IRF IRRIGATION LANDSCAPING & MAINT LLC  
 2331 N STATE RD 7 STE 203  
 LAUDERHILL, FL 33313

FEE: 75.00

CERTIFIED CONTRACTOR IRRIGATION SPRINKLER

ID #0095143  
02/16/06

LF

FOLD HERE

SIGNATURE:

ATTEST:

CONSTRUCTION INDUSTRY LICENSING BOARD  
OF PALM BEACH COUNTY

1) PLEASE CHECK ALL INFORMATION TO INSURE THAT IT IS CORRECT

2) CERTIFICATE MUST BE SIGNED

3) FOLD THE CARD WHERE INDICATED FOR EASE IN CARRYING

\* 2015-2006

ST. LUCIE COUNTY OCCUPATIONAL LICENSE  
BOB DAVIS, CPA, CGFO, CFC, ST. LUCIE COUNTY TAX COLLECTOR

ACCOUNT 1799-20020002

EXPIRES SEP 30, 2006

INES

INES

F  
SS

IV  
DIV

VG  
SS

ROOMS

SEATS

EMPLOYEES 21

1799-GENERAL CONTRACTOR

2945 W Midway Rd  
St Lucie County

Troy Drawdy DBA Drawdy  
Brothers Construction II, Inc.  
Drawdy, Troy  
9701 Muller Rd  
Fort Pierce FL 34981

CG-CA13797

X RENEWAL  
NEW LICENSE  
TRANSFER  
ORIGINAL TAX 25.00

AMOUNT  
PENALTY  
COLLECTION COST  
TOTAL 25.00

3405-421-001-000/2


Please see back for additional information

P00000041342

PAID 08/12/2005

99-20050812-164480

25.00



DETACH HERE

442551

STATE OF FLORIDA

DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION  
CONSTRUCTION INDUSTRY LICENSING BOARD

SEQ# 104060901270

DATE	BATCH NUMBER	LICENSE NBR
9/2004	1030711986	CGCA13797

GENERAL CONTRACTOR  
listed below IS CERTIFIED  
under the provisions of Chapter 489 FS  
Expiration date: AUG 31, 2006



TROY, TROY WAYNE  
BROTHERS CONSTRUCTION II, INC.  
W MIDWAY ROAD  
PIERCE FL 34981

EB BUSH

DIANE CARR



STATE OF FLORIDA

DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION

CONSTRUCTION INDUSTRY LICENSING BOARD  
1940 NORTH MONROE STREET  
TALLAHASSEE FL 32399-0783

(850) 487-1395

BROWN, JOHN PETER  
INDUSTRIAL STEEL FABRICATORS INC  
P O BOX 61597  
JACKSONVILLE FL 32236-1597

DETACH HERE

AC# 2602736

STATE OF FLORIDA

DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION  
CONSTRUCTION INDUSTRY LICENSING BOARD

SEQ# L06060100986

DATE	BATCH NUMBER	LICENSE NBR
06/01/2006	057035233	CGC053643

The GENERAL CONTRACTOR  
Named below IS CERTIFIED  
Under the provisions of Chapter 489 FS.  
Expiration date: AUG 31, 2008

BROWN, JOHN PETER  
INDUSTRIAL STEEL FABRICATORS INC  
11518 NORMANDY BLVD  
JACKSONVILLE FL 32221

JEB BUSH  
GOVERNOR

SIMONE MARSTILLER  
SECRETARY

DISPLAY AS REQUIRED BY LAW



# 2006-2007 OCCUPATION LICENSE TAX

CITY OF JACKSONVILLE/DUVA COUNTY  
MIKE HOGAN, TAX COLLECTOR

231 E FORSYTH STREET ROOM 130 JACKSONVILLE, FL 32202-3370  
PHONE: (904) 630-2080 FAX: (904) 630-4432  
WEBSITE: www.coj.net/fo

Note - A penalty is imposed for failure to keep this license exhibited conspicuously at your establishment of place of business. This license is furnished pursuant to chapter 770-77, City ordinance codes.

INDUSTRIAL STEEL FABRICATORS, INC  
INDUSTRIAL STEEL FABRICATORS, INC  
11518 NORMANDY BV  
JACKSONVILLE, FL 32221-1811

ACCOUNT NUMBER: 182240000  
LOCATION ADDRESS: 11518 NORMANDY BV  
JACKSONVILLE FL 32221-1811

DESCRIPTION: CONTRACTOR - ALL TYPES

COUNTY LICENSE DESC:	CONTRACTOR - ALL TYPES	COUNTY TAX:	45.00
MUNICIPAL LICENSE DESC:	MG 772308	MUNICIPAL TAX:	181.25
		TOTAL TAX PAID:	226.25

VALID FROM August 1, 2006 TO September 30, 2007

### \*\*\*ATTENTION\*\*\*

THIS LICENSE IS FOR OCCUPATION LICENSE TAX ONLY.  
CERTAIN OCCUPATIONS MAY REQUIRE ADDITIONAL STATE LICENSING.

This is an occupation license tax only. It does not permit the licensee to violate any existing regulatory or zoning laws of the County or City. Nor does it exempt the licensee from any other license or permit required by law. This is not a certification of the licensee's qualifications.

TAX COLLECTOR

THIS BECOMES A RECEIPT AFTER VALIDATION.

PAID-8334067.0001-0001 Q10 10/11/ 006 226.25

**2006 - 2007**

**BREVARD COUNTY OCCUPATIONAL LICENSE**  
SUBJECT TO COUNTY ZONING RESTRICTIONS  
LICENSE SHOULD BE DISPLAYED ON PREMISES

ACCOUNT NO.  
74381

THE PERSON(S) OR ENTITY BELOW:

**LICENSE PERIOD: OCTOBER 1, 2006 - SEPTEMBER 30, 2007**  
**EXPIRES: SEPTEMBER 30, 2007**

**INDUSTRIAL STEEL INC**

P O BOX 346  
MIMS FL 32754-0000

ISSUED PURSUANT AND SUBJECT TO FLORIDA STATUTES AND BREVARD COUNTY CODE  
ISSUANCE DOES NOT CERTIFY COMPLIANCE WITH ZONING OR OTHER LAWS.  
LICENSE IS SUBJECT TO REVOCATION FOR ZONING VIOLATIONS, AND / OR FAILURE TO  
MAINTAIN REGULATORY PRE-REQUISITES AS REQUIRED FOR LIC. CLASSIFICATION(S),  
OR SUBSEQUENT ACTIVITIES. NOTIFY TAX COLLECTOR UPON CLOSING OF BUSINESS.  
A PERMIT IS REQUIRED TO ADVERTISE (including with signage) "GOING OUT OF BUSINESS"

IS LICENSED AS INDICATED FOR THE FOLLOWING LOCATION:

ROD NORTHCUTT, CFC, CPM, Tax Collector, Brevard County  
P O Box 2600, Titusville, Florida 32781-2600  
(321) 264-6910

3540 INDUSTRIAL RD  
UNINCORP. DIST. 1 FL 32796-0000

UPON A CHANGE OF OWNERSHIP OR LOCATION,  
LICENSE SHOULD BE TRANSFERRED WITHIN 30 DAYS.


OWNED BY:

**INDUSTRIAL STEEL INC**

LICENSE CLASSIFICATIONS, DISCLAIMERS AND RELATED FEES:

EXEMPTIONS: NON EXEMPT

	<b>PENALTY:</b>	\$ .00
300305	GENERAL CONTR.(CERTIFIED)	
390147	METAL PRODUCTS MFG.	
590502	HAZ. WASTE GEN. SURCHARGE	
820006	2006 - 2007 LICENSE AMOUNT	\$37.00
	NEW HAZ WASTE CHARGE	\$40.00

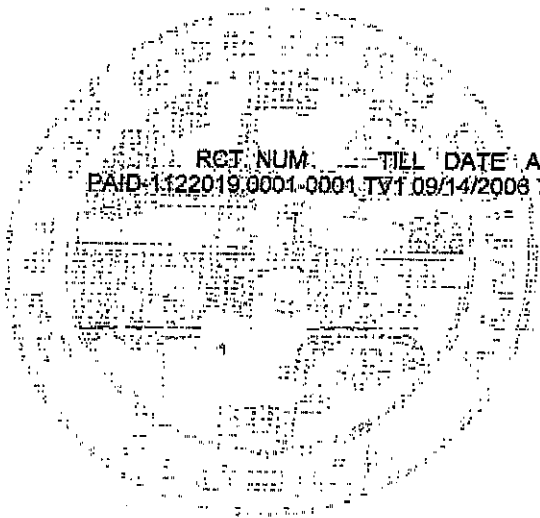

REG. NUM. --- TILL DATE : AMT PAID  
PAID-1122019.0001-0001 TV1 09/14/2006 77.00

**BRANCH OFFICES:**

Merritt Island Office, 1450 N. Courtenay Pkwy, Merritt Island, FL 32953 (321) 455-1413  
Melbourne Office, 1515 Sarno Road, Melbourne, FL 32935 (321) 258-4453  
Palm Bay Office, 2050 Eldron Blvd SE, Palm Bay, FL 32909 (321) 958-6325

**MAIN OFFICE:**

400 South St - 6th Floor, Titusville, FL 32780 (321) 264-6910, (321) 533-2199, ext. 46910



MIAMI-DADE COUNTY  
TAX COLLECTOR  
140 W. FLAGLER ST.  
14th FLOOR  
MIAMI, FL 33130

2006 OCCUPATIONAL LICENSE TAX 2007  
MIAMI-DADE COUNTY - STATE OF FLORIDA  
EXPIRES SEPT. 30, 2007  
MUST BE DISPLAYED AT PLACE OF BUSINESS  
PURSUANT TO COUNTY CODE CHAPTER 8A - ART. 9 & 10

FIRST-CLASS  
U.S. POSTAGE  
PAID  
MIAMI, FL  
PERMIT NO. 21

THIS IS NOT A BILL-DO NOT PAY

054830-6  
BUSINESS NAME / LOCATION  
INSTITUTIONAL PRODUCTS INC  
1011 NW 6 ST  
33030 HOMESTEAD

RENEWAL  
LICENSE NO. 054830-6

OWNER  
INSTITUTIONAL PRODUCTS INC  
Sec. Type of Business  
206 MANUFACTURING

EMPLOYEES  
5

THIS IS AN OCCUPATIONAL  
TAX ONLY. IT DOES NOT  
PERMIT THE LICENSEE TO  
VIOLATE ANY EXISTING  
REGULATORY OR ZONING  
LAWS OF THE COUNTY OR  
CITY. NOR DOES IT  
EXEMPT THE LICENSEE  
FROM ANY OTHER LICENSE  
OR PERMIT REQUIRED BY  
LAW. THIS IS NOT A  
CERTIFICATION OF THE  
LICENSEE'S QUALIFICA-  
TION.


DO NOT FORWARD

INSTITUTIONAL PRODUCTS INC  
1011 NW 6 ST  
HOMESTEAD FL 33030

PAYMENT RECEIVED  
MIAMI-DADE COUNTY TAX  
COLLECTOR

08/02/2006  
6006000298  
000045.00

SEE OTHER SIDE





AC# 2656059

STATE OF FLORIDA

DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION  
CONSTRUCTION INDUSTRY LICENSING BOARD

SEQ# L06071300902

DATE	BATCH NUMBER	LICENSE NBR
07/13/2006	050815944	EGC023527

The GENERAL CONTRACTOR  
Named below IS CERTIFIED  
Under the provisions of Chapter 489 FS.  
Expiration date: AUG 31, 2008

WEIDENBENNER, PERRY E.  
SPD CONSTRUCTION INC  
9900 W SAMPLE ROAD SUITE 300  
CORAL SPRINGS FL 33065

JEE BUSH  
GOVERNOR

DISPLAY AS REQUIRED BY LAW

SIMONE MARSTILLER  
SECRETARY

FAC# 2662333

STATE OF FLORIDA  
DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION  
CONSTRUCTION INDUSTRY LICENSING BOARD SEQ# L06071700587

DATE	BATCH NUMBER	LICENSE NBR
07/17/2006	060012850	EGC0008571

The GENERAL CONTRACTOR  
Named below IS CERTIFIED  
Under the provisions of Chapter 489 FS.  
Expiration date: AUG 31 2008

COVERT, JAMES E JR  
CO MAN CAULKING & WATERPROOFING INC  
2950 COMMERACES PARK DR  
BOYTON BEACH FL 33426

JEB BUSH  
GOVERNOR

SIMONE MARSTILLER  
SECRETARY

DISPLAY AS REQUIRED BY LAW

2006-00071

STATE OF FLORIDA

OC-032

**PALM BEACH COUNTY  
OCCUPATIONAL LICENSE**

CLASSIFICATION

**EXPIRES: SEPTEMBER - 30 - 2007**

COMAN CAULKING & WATERPROOFING  
INC  
COVERT JAMES E JR

\*\* LOCATED AT  
2950-3 COMMERCE PARK DR  
BOYNTON BEACH FL 33426-8779

CNTY \$27.50

TOTAL \$27.50

Is hereby licensed at above address for the period beginning on the first day of October and ending on the thirtieth day of September to engage in the business, profession or occupation of:  
  
GENERAL CONTRACTOR  
  
CGC008571

**THIS IS NOT A BILL - DO NOT PAY**

PAID. PBC TAX COLLECTOR  
\$27.50 OCC 049 025455 08-17-2006

Peter H. Carney  
TAX COLLECTOR, PALM BEACH COUNTY

**THIS LICENSE VALID ONLY WHEN RECEIPTED BY  
TAX COLLECTOR**

2006-00072

STATE OF FLORIDA

CW-001

PALM BEACH COUNTY

CLASSIFICATION

**OCCUPATIONAL LICENSE**

**EXPIRES: SEPTEMBER - 30 - 2007**

COMAN CAULKING & WATERPROOFING  
INC  
COVERT JAMES E JR

\*\* LOCATED AT  
2950-3 COMMERCE PARK DR  
BOYNTON BEACH FL 33426-8779

C/WIDE \$369.60

TOTAL \$369.60

Is hereby licensed at above address for the period beginning on the first day of October and ending on the thirtieth day of September to engage in the business, profession or occupation of:  
  
GENERAL CONTRACTOR  
  
CGC008571

**THIS IS NOT A BILL - DO NOT PAY**

PAID. PBC TAX COLLECTOR  
\$369.60 OCC 049 030239 08-23-2006

Peter H. Carney  
TAX COLLECTOR, PALM BEACH COUNTY

**THIS LICENSE VALID ONLY WHEN RECEIPTED BY  
TAX COLLECTOR**

10-04-2006 13.38



# PALM BEACH COUNTY TAX COLLECTOR OCCUPATIONAL LICENSE

License Year: 2000 License Number: 15061

Fee Class: OC032

Status: ACTIVE

Business Name: ALLSTATES FIREPROOFING INC

Owner Name: WERTZ WILLIAM E

<b>Business</b>	
Address:	1380 16TH ST WEST
City:	RIVIERA BEACH
State:	FL
Zip:	33404-5342
Phone:	(561) 842-8880

<b>Mail</b>	
Address:	1380 16TH ST WEST
City:	RIVIERA BEACH
State:	FL
Zip:	33404-6310

City Limits: NO

State Cert: U-11438

Fee Period: ONE YEAR

Orig Issue: 03/17/2000

**RENEWED**

Exp Date: 09/30/2007

Delq Pers Prop:

Number of: 4

Type of Business: INSULATION & ACOUSTICAL



STATE OF FLORIDA  
DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION  
CONSTRUCTION INDUSTRY LICENSING BOARD  
1940 NORTH MONROE STREET  
TALLAHASSEE FL 32399-0782

(850) 487-1395

MILANESE, JEFFREY M  
TRIPLE M ROOFING CORP  
6430 HUDSON BAY LANE  
LAKE WORTH FL 33467

STATE OF FLORIDA AC# 2769131  
DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION

CCC1326182 08/31/06 068044850

CERTIFIED ROOFING CONTRACTOR  
MILANESE, JEFFREY M.  
TRIPLE M ROOFING CORP

IS CERTIFIED under the provisions of Ch. 489 FS.  
Expiration date: AUG 31, 2008 X06029102795

DETACH HERE

AC# 2769131

STATE OF FLORIDA  
DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION  
CONSTRUCTION INDUSTRY LICENSING BOARD SEQ# 106029101795

DATE	BATCH NUMBER	LICENSE NBR.
08/31/2006	068044850	CCC1326182

The ROOFING CONTRACTOR  
Named below IS CERTIFIED  
Under the provisions of Chapter 489 FS.  
Expiration date: AUG 31, 2008

MILANESE, JEFFREY M  
TRIPLE M ROOFING CORP  
6430 HUDSON BAY LANE  
LAKE WORTH FL 33467

JEB BUSH  
GOVERNOR

SIMONE MARSTILLER  
SECRETARY

DISPLAY AS REQUIRED BY LAW

18 PAGE

MAIL BOXES ETC

09/29/2006 03:30 5614928891

AC# 2680574

STATE OF FLORIDA

DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION  
CONSTRUCTION INDUSTRY LICENSING BOARD

SEQ# D06072601127

DATE	BATCH NUMBER	LICENSE NBR
07/26/2006	068012197	CRC051328

The RESIDENTIAL CONTRACTOR  
Named below IS CERTIFIED  
Under the provisions of Chapter 489 FS.  
Expiration date: AUG 31, 2008

EWART, PETER MATTHEW  
WORKS (DON) & COMPANY INC  
P O BOX 24600  
FT LAUDERDALE FL 33307-4600

JEB BUSH  
GOVERNOR

SIMONE MARSTILLER  
SECRETARY

DISPLAY AS REQUIRED BY LAW

To: LINDA

KAUFMAN LYNN



FAX - 561 / 361 - 6979

Attn: Linda @ Kaufman byer

Okechee

12/15/06

561-361-6979



MIAMI-DADE COUNTY TAX COLLECTOR  
MAYNARD BLUMBERG  
MAYNARD BLUMBERG  
MIAMI FL 33136  
OCCUPATIONAL LICENSE TAX  
MIAMI-DADE COUNTY STATE OF FLORIDA  
EXPIRES SEPT 30, 2007  
MUST BE DISPLAYED AT PLACE OF BUSINESS  
SUBJ: MIAMI-DADE COUNTY CODE CHAPTER 219.001(3)&(4)

FIRST-CLASS  
U.S. POSTAGE  
PAID  
MIAMI, FL  
PERMIT NO. 231

THIS IS NOT A BILL-DO NOT PAY

565937-1  
BUSINESS NAME/LOCATION  
ARC ONE LLC  
1350 NW 74 ST  
33147 UNIN DADE COUNTY

RENEWAL  
LICENSE NO. 006479-0

OWNER  
ARC ONE LLC  
Sec. Type of Business  
206 MANUFACTURING

EMPLOYEES  
135


THIS IS AN OCCUPATIONAL  
TAX ONLY. IT DOES NOT  
PERMIT THE LICENSEE TO  
VIOLATE ANY EXISTING  
REGULATORY OR ZONING  
LAWS OF THE COUNTY OR  
CITIES. NOR DOES IT  
EXEMPT THE LICENSEE  
FROM ANY OTHER LICENSE  
OR PERMIT REQUIRED BY  
LAW. THIS IS NOT A  
CERTIFICATION OF THE  
LICENSEE'S QUALIFICA-  
TION.

DO NOT FORWARD

ARC ONE LLC  
LYNN TILTON  
P O BOX 380878  
MIAMI FL 33238

PAYMENT RECEIVED  
MIAMI-DADE COUNTY TAX  
COLLECTOR

08/28/2006  
60010000551  
003012850



SEE OTHER SIDE



# 2735439

STATE OF FLORIDA

DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION  
CONSTRUCTION INDUSTRY LICENSING BOARD

SEQ#L06082000205

DATE	BATCH NUMBER	LICENSE NBR
8/20/2006	058095287	CGC021798

The GENERAL CONTRACTOR  
Named below IS CERTIFIED  
Under the provisions of Chapter 489 FS.  
Expiration date: AUG 31, 2008

GORDON, MICHAEL JAY  
HURRICANE RESISTANT CONSTRUCTION INC  
12105 LYMESTONE WAY  
HOLLYWOOD FL 33026

JEB BUSH  
GOVERNOR

SIMONE MARSTILLER  
SECRETARY

DISPLAY AS REQUIRED BY LAW

FROM : SOL-A-TROL



**Peter H. Carney, Tax Collector**  
P.O. Box 3353  
West Palm Beach, FL 33402-3353  
www.pbcgov.com/tax Tel:(561) 355-2272

SOL A TROL ALUMINUM PRODUCTS  
SOLER ANTONIO L  
2005 ARCH CREEK DR  
NORTH MIAMI FL 33181-2114

License Number: **1989-05413**

Dear Business Owner:

This is your new occupational license. Please keep the upper portion for your records and detach the bottom of this form. Verify the information and display it conspicuously at your place of business, open to the view of the public.

This license is in addition to and not in lieu of any other license required by law or municipal ordinance and is subject to regulations of zoning, health, and any other lawful authority (County Ordinance Number 72-7).

Licenses may be transferred to a new owner when evidence of a sale is provided; the original license is surrendered and a transfer fee is paid.

Licenses may be transferred to a new location when proof of zoning approval is provided; the original license is surrendered and a transfer fee is paid.

Business name changes require a new license.

This license expires on **September 30, 2007**. Renewal notices are mailed at the end of July. If you do not receive the notice by the middle of August, please let us know.

I hope you have a successful year.

Tax Collector

\*\*\* DETACH AND DISPLAY BOTTOM PORTION, AND KEEP UPPER PORTION FOR YOUR RECORDS \*\*\*

**1989-05413**

STATE OF FLORIDA  
PALM BEACH COUNTY  
**OCCUPATIONAL LICENSE**  
**EXPIRES: SEPTEMBER - 30 - 2007**

CW-008  
CLASSIFICATION

SOL A TROL ALUMINUM PRODUCTS  
SOLER ANTONIO L

\*\*\* LOCATED AT  
4101 NW 132ND STREET  
MIAMI FL 33054

C/WIDE \$185.85

TOTAL \$185.85

Is hereby licensed at above address for the period beginning on the first day of October, and ending on the thirtieth day of September to engage in the business, profession or occupation of  
**GLASS & GLAZING CONTR**  
U15259

**THIS IS NOT A BILL - DO NOT PAY**  
PAID. PBC TAX COLLECTOR  
\$185.85 OCC 849 046877 09-19-2006

Peter H. Carney

THIS LICENSE VALID ONLY WHEN RECEIVED BY

AU# 2710100

STATE OF FLORIDA

DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION  
CONSTRUCTION INDUSTRY LICENSING BOARD

SEQ#L0608110124

DATE	BATCH NUMBER	LICENSE NBR
08/11/2006	060100851	CGC013538

The GENERAL CONTRACTOR  
Named below IS CERTIFIED  
Under the provisions of Chapter 489 FS.  
Expiration date: AUG 31, 2008

SANTEIRO, JUAN C  
ATLANTIC INTERIOR CONTRING INC  
12601 SW 5TH CT  
FT LAUDERDALE FL 33325

JEB BUSH  
GOVERNOR

SIMONE MARSTILLER  
SECRETARY

DISPLAY AS REQUIRED BY LAW

FROM : Pallais Construction Co., Inc. PHONE NO. : 305+207 7020

Dec. 12 2006 01:42PM P2

5H

Board of County Commissioners, Broward County Florida  
BROWARD COUNTY OCCUPATIONAL LICENSE TAX

01398

FORM NO. 401-280/AC 25-061  
RV200625413 (Rev. 3/06)

FOR PERIOD OCTOBER 1, 2006 THRU SEPTEMBER 30, 2007

RENEWAL     TRANSFER    SEC # 18 / 187  
 NEW    DATE BUSINESS OPENED 03/13/98

STATE OR COUNTY CERT/REG # 42-3227-TPI  
Business Location Address:  
14201 SW 55 ST  
DADE COUNTY    33175-0000  
BUSINESS PHONE: (954) 207-7070

TAX	54.00
BACK TAX	
PENALTY	
T.C. FEE	
TRANSFER	
TOTAL	54.00

PENALTIES IF PAID	
OCT. - 10%	NOV. - 15%
DEC. - 20%	* After DEC. 31 - 25%
* Plus Tax Collection Fee of up to \$25.00 Based on Cost of License if Paid On or After November 30.	

ACCOUNT NUMBER  
187-0000389

THIS LICENSE MUST BE CONSPICUOUSLY DISPLAYED  
TO PUBLIC VIEW AT THE LOCATION ADDRESS ABOVE.

PALLAIS CONSTRUCTION INC  
LUIS PALLAIS  
14201 SW 55 STREET  
MIAMI FL.    33175-0000



TYPE OF LICENSE TAX PAID  
SPEC SLDR TILE & MARBLE CONTRA  
16 UNITS

**2006 - 2007**

BROWARD COUNTY REVENUE COLLECTION  
115 S. Andrews Avenue, Governmental Center Annex  
FORT LAUDERDALE, FL 33301  
www.broward.org/revenue

PAYMENT RECEIVED AS VALIDATED ABOVE

\*SEE INSTRUCTIONS ON BACK OF LAST COPY

PAID 08/11/06 7009169.0001

54.00

MIAMI-DADE COUNTY  
TAX COLLECTOR  
140 W. FLAGLER ST.  
14th FLOOR  
MIAMI, FL 33130

2005 OCCUPATIONAL LICENSE TAX  
MIAMI-DADE COUNTY - STATE OF FLORIDA  
EXPIRES SEPT. 30, 2006  
MUST BE DISPLAYED AT PLACE OF BUSINESS  
PURSUANT TO COUNTY CODE CHAPTER 8A - ART. 9 & 10

FIRST-CLASS  
U.S. POSTAGE  
PAID  
MIAMI, FL  
PERMIT NO. 23

191399-6  
BUSINESS NAME / LOCATION  
SUPERIOR INTERIOR SYSTEMS INC  
20328 NE 16 PL  
33179 UNIN DADE COUNTY

THIS IS NOT A BILL-DO NOT PAY  
RENEWAL  
LICENSE NO. 191399-6  
CC # 000016024

OWNER  
SUPERIOR INTERIOR SYSTEMS INC  
Sec. Type of Business  
196 SPECIALTY BUILDING CONTRACTOR  
WORKER/S  
10


DO NOT FORWARD  
SUPERIOR INTERIOR SYSTEMS INC  
20328 NE 16 PL  
MIAMI FL 33179

THIS IS AN OCCUPATIONAL  
TAX ONLY. IT DOES NOT  
PERMIT THE LICENSEE TO  
REGISTER IN ANY OTHER  
REGULATORY OR EXISTING  
LAW OF THE COUNTY OR  
CITIES. NOR DOES IT  
EXEMPT THE LICENSEE  
FROM ANY OTHER LICENSE  
OR PERMIT REQUIRED BY  
LAW. THIS IS NOT THE  
CERTIFICATION OF THE  
LICENSEE'S QUALIFICA-  
TION.

PAYMENT RECEIVED  
MIAMI-DADE COUNTY TAX  
COLLECTOR:

09/22/2005  
00210000088  
000075.00

SEE OTHER SIDE



MIAMI-DADE COUNTY  
TAX COLLECTOR  
140 W. FLAGLER ST.  
14th FLOOR  
MIAMI, FL 33130

2005 MUNICIPAL CONTRACTOR'S  
OCCUPATIONAL LICENSE  
MIAMI-DADE COUNTY - STATE OF FLORIDA  
PURSUANT TO DADE COUNTY CODE SEC. 10-24  
EXPIRES SEPT. 30, 2006

FIRST-CLASS  
U.S. POSTAGE  
PAID  
MIAMI, FL  
PERMIT NO. 23

THIS IS NOT A BILL-DO NOT PAY  
CC NO: 000016024

LICENSE NO. 30-1913996  
BUSINESS NAME / LOCATION

SUPERIOR INTERIOR SYSTEMS INC  
20328 NE 16 PL  
OWNER : SUPERIOR INTERIOR SYSTEMS INC

IS HEREBY LICENSED TO DO  
BUSINESS AS A CONTRACTOR  
AS SPECIFIED HEREON.

SEE BACK OF LICENSE FOR  
A LIST OF NON-PARTICIPATING  
MUNICIPALITIES

DO NOT FORWARD

Licensee must  
register in the city  
where work is to  
be done.

SUPERIOR INTERIOR SYSTEMS INC  
20328 NE 16 PL  
MIAMI FL 33179

PAYMENT RECEIVED  
MIAMI-DADE COUNTY TAX  
COLLECTOR  
09/22/2005  
00210000089  
000175.00

**BUILDING CODE COMPLIANCE OFFICE**  
BUSINESS CERTIFICATE OF COMPETENCY

**CTQB** Construction Trades and Qualifying Board

Qualifying Agent: COOPER RICHARD P JR  
License Number: 000016024

Contractor Name: SUPERIOR INTERIOR SYSTEMS INC  
Exp. Date: 09/30/2006

*Hermínio F. Gonzalez P.E.*  
Hermínio F. Gonzalez P.E.  
Secretary of the Board

VALID FOR CONTRACTING

Is certified under the provisions of Chapter 10 of Miami-Dade County

MIAMI-DADE COUNTY



# CITY OF DEERFIELD BEACH

OCCUPATIONAL LICENSE

2006-2007

LICENSE NO.  
07-00023562

NEW                      RENEWAL    X

DATE ISSUED            8/28/06

LICENSE FEE            117.60


DELINQUENT CHG.       0.00

TRANSFER FEE           0.00

**TOTAL AMOUNT PAID            117.60**

LICENSE ISSUED FOR THE PERIOD  
OCTOBER 1 2006 SEPTEMBER 30 2007

OWNER            BROOKSIDE 1, INC.  
CONTROL NO.      175490  
BUSINESS NAME    BROOKSIDE 1, INC.  
LOCATION            241 GOOLSBY BLVD  
CLASSIFICATION   BUSINESS OFFICE  
*OFFICE USE ONLY SHOWROOM*



BROOKSIDE 1, INC.  
4554 NW 25 WAY  
BOCA RATON FL 33434

**LICENSE MUST BE CONSPICUOUSLY  
DISPLAYED TO PUBLIC VIEW AT  
BUSINESS LOCATION**

TRANSFER FEE            11.76

*Notice: This license becomes NULL and VOID if ownership, business name, or address is changed. Licensee must apply to License Department for Transfer.*

*Mark Erjavac*

ORDER OF  
MAGISTRATE  
MAY 11 2004  
ONLINE S. AND



**CERTIFICATE OF COMPETENCY**

**BELOWARD**

**PROFESSIONAL**

**MARK ERJAVAC**

**SPECIALIZING IN EXTERIOR**

**GRAY'S PAINTING**

**CC# 014-12714**

**Expires 01/2008**

**REL. 1/20/04**

**CC# 014-12714**





### CITY OF TARPON SPRINGS

324 EAST PINE STREET  
TARPON SPRINGS, FLORIDA 34689

### OCCUPATIONAL LICENSE

BUSINESS ADDRESS: 40347 US HIGHWAY 19 N # 117  
LICENSE NUMBER: 07-00047792  
ADMINISTRATIVE OFFICE - C

LICENSE FEE: 71.75  
PENALTY: 0.00  
TOTAL PAID: 71.75

COMMENTS:  
RESTRICTIONS:

FLORIDA CHALKBOARD CO, INC  
40347 US HIGHWAY 19 N #117  
TARPON SPRINGS FL 34689-4840

FLORIDA CHALKBOARD CO INC  
1428 E SEMORAN SUITE 103  
ALTAMONTE SPRINGS FL 32704

**PLEASE POST IN A CONSPICUOUS PLACE**

Expires September 30<sup>th</sup> of Year Notated in License Number

ELLEN S. POSIVACH, CITY MANAGER

BUSINESS ADDRESS: 40347 US HIGHWAY 19 N # 117  
LICENSE NUMBER: 07-00047792  
ADMINISTRATIVE OFFICE - C

LICENSE FEE: 71.75  
PENALTY: 0.00  
TOTAL PAID: 71.75


COMMENTS:  
RESTRICTIONS:

FLORIDA CHALKBOARD CO, INC  
40347 US HIGHWAY 19 N #117  
TARPON SPRINGS FL 34689-4840

FLORIDA CHALKBOARD CO INC  
1428 E SEMORAN SUITE 103  
ALTAMONTE SPRINGS FL 32704



Walker Design

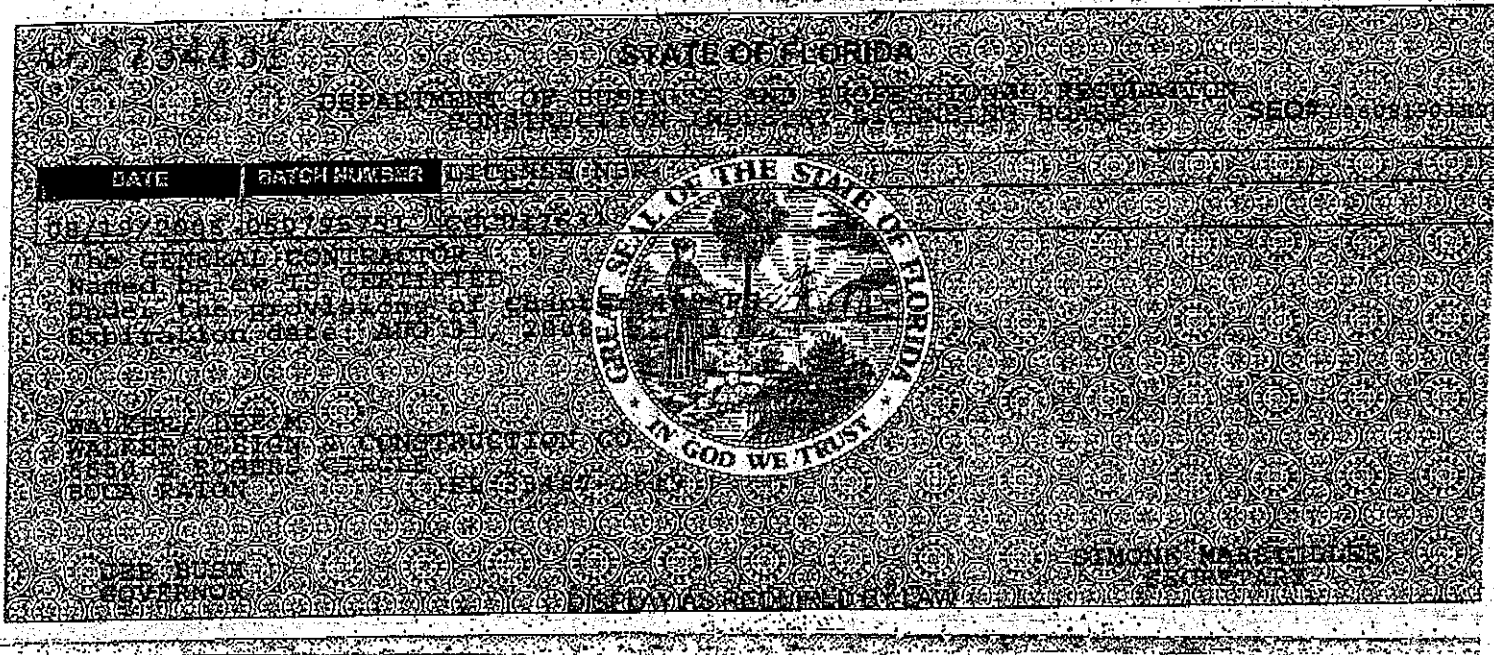

**STATE OF FLORIDA  
DEPARTMENT OF FINANCIAL SERVICES  
DIVISION OF STATE FIRE MARSHAL  
TALLAHASSEE, FLORIDA  
FIRE EXTINGUISHER PERMIT**



**THIS CERTIFIES THAT:** ORLANDO ALFONSO  
**EMPLOYER:** TRIANGLE FIRE INC  
 7720 NW 53RD STREET  
 MIAMI, FL 33166  
**LICENSE NUMBER:** 58788900012001 - FIRE EQUIPMENT CLASS A LICENSE

HAS COMPLIED WITH FLORIDA STATUTES AND IS QUALIFIED FOR THE TYPE AND CLASS SHOWN HEREIN TO SERVICE, RECHARGE, REPAIR, INSTALL OR INSPECT PORTABLE FIRE EXTINGUISHERS, AS APPLICABLE. THE PERSON NAMED IN THIS PERMIT SHALL NOT PERFORM WORK ANY MORE EXTENSIVE THAN THE EMPLOYER NAMED HEREIN.

Chief Financial Officer

01	01	2006	09	01	Dade	64598400022001	6833450002	12	31	2007
Issue Date		Type	Class	County		License/Permit Number	Application #	Expire Date		

**STATE OF FLORIDA  
DEPARTMENT OF FINANCIAL SERVICES  
DIVISION OF STATE FIRE MARSHAL  
TALLAHASSEE, FLORIDA  
FIRE EXTINGUISHER PERMIT**



**THIS CERTIFIES THAT:** ORLANDO ALFONSO  
**EMPLOYER:** TRIANGLE FIRE INC  
 7720 NW 53RD STREET  
 MIAMI, FL 33166  
**LICENSE NUMBER:** 58789100012001 - FIRE EQUIPMENT CLASS D LICENSE

HAS COMPLIED WITH FLORIDA STATUTES AND HAS QUALIFIED FOR THE TYPE AND CLASS SHOWN HEREON TO SERVICE, REPAIR, INSTALL, INSPECT ALL TYPES OF PRE-ENGINEERED FIRE EXTINGUISHING SYSTEMS.

Chief Financial Officer

01	01	2006	09	04	Dade	64598400012001	6833460002	12	31	2007
Issue Date		Type	Class	County		License/Permit Number	Application #	Expire Date		



# CITY OF WEST PALM BEACH 2006-07 LICENSE / CERTIFICATE OF USE

**NOT TRANSFERABLE**  
CITY OF WEST PALM BEACH  
110 BOX 1147 WEST PALM BEACH, FL 33411

179G039300-5  
ELECHS INC  
4149 SW 47TH AVE # A

REGISTRAR  
NO WK REQ A CONTR LICENSE

LICENSE NO	CATEGORY	DESCRIPTION	FEES
10042	1789A	REG MOBILE CONSTRUCTION RELATED SVCS	66.15
CHANGES		PENALTIES	0.00
TOTAL			66.15
** PAID			66.15
** BAL **			0.00

**EXPIRES  
SEPTEMBER 30,  
2007**

**THIS DOCUMENT NOT VALID  
UNTIL FUNDS ARE COLLECTED**



PO. BOX 5917  
DAVIE, FL 33310-5917

**OCCUPATIONAL LICENSE**

NAME AND LOCATION OF LICENSEE

ELECHS, INC.  
4149 SW 47 AVE A  
DAVIE FL 33314

PERMIT STD  
U.S. POSTAGE  
PAID  
MANASOTA, FL  
PERMIT #710


CONTROL NO.	LICENSE TYPE	BEGINNING	ENDING ON	PHONE NUMBER
0012978	REGULAR	10/01/2006	7/30/2007	954-689-8668
LICENSE #	CODE	DESCRIPTION		
07-00015476	07300	DISTRIBUTORS; FURN/BLDG/APPLI/FOOD ETC		

Reference:

E L EDWARDS

TO:  
ELECHS, INC.  
4149 SW 47 AVE A  
DAVIE FL 33314

0001



FROM 954-689-7188

Board of County Commissioners, Broward County Florida  
BROWARD COUNTY OCCUPATIONAL LICENSE TAX

00422

FORM NO. 401-280/AC 25-061  
RV200625413 (Rev. 3/06)

FOR PERIOD OCTOBER 1, 2006 THRU SEPTEMBER 30, 2007.

RENEWAL     TRANSFER    SEC # 377.377  
 NEW    DATE BUSINESS OPENED 10/14/06  
STATE OR COUNTY CERT/REG # \_\_\_\_\_  
Business Location Address:

TAX	45.00
BACK TAX	
PENALTY	
T/C FEE	
TRANSFER	
<b>TOTAL</b>	<b>45.00</b>

PENALTIES IF PAID	
OCT. - 10%	NOV. - 15%
* DEC. - 20%	* After DEC. 31 - 25%
* Plus Tax Collection Fee of up to \$25.00 Based on Cost of License if Paid On or After November 30.	

4149 SW 47 AVE A    33314  
DAVIE, FL  
PHONE: (954) 689-2588

ACCOUNT NUMBER  
377-00015476

THIS LICENSE MUST BE CONSPICUOUSLY DISPLAYED  
TO PUBLIC VIEW AT THE LOCATION ADDRESS ABOVE.

ELECHS INC  
EDWARDS E L  
4149 SW 47 AVENUE STE A  
DAVIE FL 33314



TYPE OF LICENSE TAX PAID

BROWARD COUNTY REVENUE COLLECTION  
115 S. Andrews Avenue, Governmental Center Annex  
FORT LAUDERDALE, FL 33301  
www.broward.org/revenue

**2006 - 2007**

PAYMENT RECEIVED AS VALIDATED ABOVE

\*SEE INSTRUCTIONS ON BACK OF LAST COPY

PAID 08/16/06 700422310001

45.00

**PALM BEACH COUNTY CONTRACTORS  
CERTIFICATE OF COMPETENCY**

EXPIRES SEPTEMBER 30, 20 07

AUDIT CONTROL NUMBER	A-0559213	CERTIFICATE NUMBER	0-14871
----------------------	-----------	--------------------	---------

NAME JANICE G DI FACIA  
FIRM FULL MOON OVER FLORIDA INC

11894 150TH CT N  
JUPITER, FL

33478

1) PLEASE CHECK ALL INFORMATION TO INSURE THAT IT IS CORRECT

2) CERTIFICATE MUST BE SIGNED

3) FOLD THE CARD WHERE INDICATED FOR EASE IN CARRYING

FEE : 180.00

CERTIFIED CONTRACTOR: SIGN CONTRACTOR, NON-ELECTRICAL  
ID #0008424  
09/19/05 SMM

FOLD HERE

SIGNATURE: *J. W.*

ATTEST: *B. M...*

CONSTRUCTION INDUSTRY LICENSING BOARD  
OF PALM BEACH COUNTY



# 2006-2007 OCCUPATION LICENSE TAX

CITY OF JACKSONVILLE/DUVAL COUNTY  
MIKE HOGAN, TAX COLLECTOR

231 E FORSYTH STREET ROOM 130 JACKSONVILLE, FL 32202-3370  
PHONE: (904) 630-2080 FAX: (904) 630-1432  
WEBSITE: www.coj.net/tc

Note - A penalty is imposed for failure to keep this license exhibited conspicuously at your establishment of place of business. This license is furnished pursuant of chapter 770-772 City ordinance codes.

NEWTON SEATING CO INC  
MICHAEL C BATES, PRES  
PO BOX 2858  
JACKSONVILLE, FL 32203-2858

*Linda*

ACCOUNT NUMBER: 260920000  
LOCATION ADDRESS: 2344 HARPER ST  
JACKSONVILLE FL 32204-1714

DESCRIPTION: TRADING-TANG PP DIST WHLSL

COUNTY LICENSE DESC:	TRADING-TANG PP DIST WHLSL	COUNTY TAX:	30.00
MUNICIPAL LICENSE DESC:	MC 772.334-2	MUNICIPAL TAX:	43.75
		TOTAL TAX PAID:	73.75

VALID FROM August 1, 2006 TO September 30, 2007

### \*\*\*ATTENTION\*\*\*

THIS LICENSE IS FOR OCCUPATION LICENSE TAX ONLY.  
CERTAIN OCCUPATIONS MAY REQUIRE ADDITIONAL STATE LICENSING.

This is an occupation license tax only. It does not permit the licensee to violate any existing regulatory or zoning laws of the County or City. Nor does it exempt the licensee from any other license or permit required by law. This is not a certification of the licensee's qualifications.

*Mike Hogan*

TAX COLLECTOR

THIS BECOMES A RECEIPT AFTER VALIDATION.

PAID-8326246.0001-0001 A15 10/06/2006 73.75

ATTN:  
LINDA

311 18112

FORM NO. 401-2800C 28-051  
RZ10025413 (Rev. 3/06)

FOR PERIOD OCTOBER 1, 2006 THRU SEPTEMBER 30, 2007

Board of County Commissioners, Broward County Florida  
BROWARD COUNTY OCCUPATIONAL LICENSE TAX

444 4444

RENEWAL  TRANSFER SEC # 333 / 333

NEW DATE BUSINESS OPENED 11/13/06

STATE OR COUNTY CERTIFIC # \_\_\_\_\_  
Business Location Address:

ADDRESS: 101 EAST 17TH AVENUE  
CORP CENTER BUILDING 1000  
SUITE 1000 WILMINGTON, DE 19801

THIS LICENSE MUST BE CONSPICUOUSLY DISPLAYED  
TO PUBLIC VIEW AT THE LOCATION ADDRESS ABOVE

TAX	333.00
BACK TAX	
PENALTY	
TC FEE	
TRANSFER	
TOTAL	333.00

PENALTIES PAID:	
OCT - 10%	NOV - 15%
DEC - 20%	* APRIL DEC. 31 - 25%
* Plus Tax Collection Fee of up to \$25.00	
Based on Cost of License if Paid	
On or After November 30.	
ACCOUNT NUMBER	333.00

INTERNATIONAL STRANGE & MATHEMATICS  
SERIES IN GARAGE VP  
226 S. WILMINGTON TRAIL  
CORP CENTER BUILDING 1000 WILMINGTON, DE 19801

**BROWARD COUNTY**  
TYPE OF LICENSE TAX PAID  
MISCELLANEOUS BLM/PROG. EXPN/MSG/INTS

**2006 - 2007**

BROWARD COUNTY REVENUE COLLECTION  
143 S. Andrews Avenue-Governmental Center Annex  
FORT LAUDERDALE, FL 33301  
www.broward.org/revenue

PAYMENT RECEIVED AS VALIDATED ABOVE \*SEE INSTRUCTIONS ON BACK OF LAST COPY

PAID 09/05/06 7012321.0001

33.00



STATE OF FLORIDA

DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION

BUREAU OF ELEVATOR SAFETY  
1940 NORTH MONROE STREET  
NORTHWOOD CENTRE  
TALLAHASSEE

FL 32399-1013

850-487-1395

THYSSENKRUPP ELEVATOR CO - RIVIERA BEACH  
P O BOX 600002  
ATTN TAX DEPARTMENT  
MARIETTA GA 30006-6002

RECEIVED

JUL 25 2006



STATE OF FLORIDA AC# 2668159  
DEPARTMENT OF BUSINESS AND  
PROFESSIONAL REGULATION

ELCO30

07/20/06 00000000

ELEVATOR COMPANY  
THYSSENKRUPP ELEVATOR CO - RIVI

ELEVATOR COMPANY  
REQUIRED TO CARRY OR BE COVERED  
BY GENERAL LIABILITY INSURANCE

IS REGISTERED under the provisions of Ch. 399  
Expiration date: JUL 1, 2007 L06072003611

DETACH HERE

C# 2668159

STATE OF FLORIDA

DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION  
BUREAU OF ELEVATOR SAFETY

SEQ#L06072003611

DATE	BATCH NUMBER	LICENSE NBR
07/20/2006	000000000	ELCO30

The ELEVATOR COMPANY  
Named below IS REGISTERED  
Under the provisions of Chapter 399 FS.  
Expiration date: JUL 1, 2007  
REQUIRED TO CARRY OR BE COVERED  
GENERAL LIABILITY INSURANCE

NON-

TRANSFERABLE

THYSSENKRUPP ELEVATOR CO - RIVIERA BEACH  
7567 CENTRAL INDUSTRIAL DR  
RIVIERA BEACH FL 33404



STATE OF FLORIDA  
 DEPARTMENT OF FINANCIAL SERVICES  
 DIVISION OF STATE FIRE MARSHAL  
 TALLAHASSEE, FLORIDA  
 CERTIFICATE OF COMPETENCY



THIS CERTIFIES THAT: ROBERT E FARMER JR  
 3300 AVE K  
 RIVIERA BEACH, FL 33404

BUSINESS ORGANIZATION: FARMER & IRWIN CORPORATION

CONTRACTOR INCLUDES THE EXECUTION OF CONTRACTS REQUIRING THE ABILITY, EXPERIENCE, KNOWLEDGE, SCIENCE, AND SKILL TO INTELLIGENTLY LAYOUT, FABRICATE, INSTALL, INSPECT, ALTER, REPAIR, OR SERVICE ALL TYPES OF FIRE PROTECTION SYSTEMS, EXCLUDING PRE-ENGINEERED SYSTEMS.

Chief Financial Officer

07	01	2006	07	15	Palm Beach	06253800011997	708420001	150.00	06	30	2008
Issue Date		Type	Class	County	License/Permit Number	Application #	Taxes & Fees	Expire Date			

DETACH HERE

AC# 2651051

STATE OF FLORIDA

DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION  
CONSTRUCTION INDUSTRY LICENSING BOARD

SEQ# L0607100

DATE	BATCH NUMBER	LICENSE NBR
07/10/2006	068005891	CFC020327



The PLUMBING CONTRACTOR  
Named below IS CERTIFIED  
Under the provisions of Chapter 489 FS.  
Expiration date: AUG 31, 2008

IRWIN, STEVEN RICHARD  
FARMER & IRWIN CORP  
3300 AVENUE K  
P O BOX 10117  
RIVIERA BEACH

FL 33404-2138

JEB BUSH  
GOVERNOR

SIMONE MARSTILLER  
SECRETARY

DISPLAY AS REQUIRED BY LAW

DETACH HERE

AC# 2586078

STATE OF FLORIDA

DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION  
CONSTRUCTION INDUSTRY LICENSING BOARD

SEQ# L0605150008

DATE	BATCH NUMBER	LICENSE NBR
05/15/2006	050653298	CMC1249623

The MECHANICAL CONTRACTOR  
Named below IS CERTIFIED  
Under the provisions of Chapter 489, FS.  
Expiration date: AUG 31, 2008

IRWIN, STEVEN RICHARD  
FARMER & IRWIN CORP  
3300 AVENUE K  
P O BOX 10117  
RIVIERA BEACH FL 33404-2138

JEB BUSH  
GOVERNOR

SIMONE MARSTILLER  
SECRETARY


DISPLAY AS REQUIRED BY LAW

032637756 (STATE OF FLORIDA)  
 DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION  
 ELECTRICAL CONTRACTORS LICENSING BOARD

DATE	BATCH NUMBER	LICENSE NBR
08/04/2006	060085330	66902878

The ELECTRICAL CONTRACTOR  
 Named below IS CERTIFIED  
 Under the provisions of Chapter  
 Expiration date: AUG 31, 2008

BY: SHAWN WILKINSON  
 EASTRAC ELECTRIC CORPORATION  
 810 SAUNN STREET SUITE 25  
 HUNTER FL 32110



JEB BUSH  
 GOVERNOR

SEYMOUR MARK MILLER  
 SECRETARY

DISPLAY AS REQUIRED BY LAW

TAB 9



THE SCHOOL DISTRICT OF PALM BEACH COUNTY
Beneficial Interest and Disclosure of Ownership Affidavit

Bid No. Project No / Title 2151-8307 Okeechewee Middle School Classroom Addition
Corporate Name Kaufman Lynn, Inc. General Contractors Tax FEIN No. 65-0098115

Before me, the undersigned authority, personally appeared, Stephen L. Haskins, CFO, ("Corporate Representative") this 1 day of February, 2007, who, first being duly sworn, as required by law, subject to the penalties prescribed for perjury, deposes and says:

- 1) Corporate Representative has read the contents of this Affidavit, has actual knowledge of the facts contained herein, and states that the facts contained herein are true, correct, and complete.
2) The following is a list of every "person" (as defined in Section 1.01(3), Florida Statutes to include individuals, children firms, associates, joint adventures, partnerships, estates, trusts, business trusts, syndicates, fiduciaries, corporations and all other groups and combinations) holding 5% or more of the beneficial interest in the disclosing entity: (If more space is needed, attach separate sheet)

A. Persons or corporate entities owning 5% or more:

Table with 3 columns: Name, Address, Percentage. Row 1: Michael I. Kaufman, 622 Banyan Trail, Suite 300, Boca Raton, FL 33431, 100%.

B. Persons or corporate entities who hold by proxy the voting power of 5% or more:

Table with 3 columns: Name, Address, Percentage. Multiple empty rows for entry.

C. Stock held for others and for whom held:

Table with 3 columns: Name, Address, Percentage. Multiple empty rows for entry.

CORPORATE REPRESENTATIVE

By: [Signature]

SWORN TO and subscribed before me this 1 day of February, 2007, by Stephen L. Haskins. Such person(s) (Notary Public must check applicable box).

[X] is/are personally known to me. [ ] produced a current driver license(s). [ ] produced as identification. (NOTARY PUBLIC SEAL)

NOTARY PUBLIC-STATE OF FLORIDA
Laura A. Sullivan
Commission # DD472296
Expires: SEP 15, 2009
Bonded Thru Atlantic Bonding Co., Inc

[Signature]
Notary Public
Laura A Sullivan
(Print Type or Stamp Name of Notary Public)

---

---

## Trench Safety Act Compliance Statement

---

---

**Project Name:** Okeeheelee Middle School Classroom Addition

**Project Number** 2151-8307

**Project Location:** 2200 Pinehurst Drive, Greenacres, FL 33413

### Instructions

Chapter 90-96 of the Laws of Florida requires all contractors engaged by The School District of Palm Beach County to comply with Occupational Safety and Health Administration Standard 29 C.F.R.s. 1926.650 Subpart P. All prospective contractors are required to sign the compliance statement and provide compliance cost information where indicated below. This cost for complying with the Trench Safety Act must be incorporated into this project's base bid as shown in section 00310 of this document.

This form must be certified in the presence of a notary public or other officer authorized to administer oaths.

---

### Certification

1. I understand that Chapter 90-96 of the Laws of Florida (The Trench Safety Act) requires me to comply with OSHA Standard 29 C.F.R.s. 1926.650 Subpart P. I will comply with the Trench Safety Act, and I will design and provide trench safety systems at all trench excavations in excess of five (5) feet in depth for this project.

2. The estimated cost imposed by compliance with the Trench Safety Act will be:

**Two Thousand Five Hundred** Dollars **\$2,500**

3. The amount listed above has been included within the Base Cost as listed in Exhibit B of this Proposal Form.

**Certified:**

By:



(President's Signature)


**Michael I. Kaufman**

(President's Typed or Printed Name)

### Notarization

Sworn to and subscribed before me in **Boca Raton**, Florida on the **1** day of **February**, 2007.

Notary Public:



My Commission Expires: \_\_\_\_\_

NOTARY PUBLIC-STATE OF FLORIDA  
**Brenda Ruiz**  
Commission # DD492965  
Expires: DEC. 12, 2009  
Bonded thru Atlantic Bonding Co., Inc.

---

**Appendix F**

TAB 10



Construction      General Conditions

Activity ID	Description	Original Duration	Early Start	Early Finish	Total Float	2007	2008
0000	NTP	0	02APR07		0	NTP	
0470	Elevator Final Inspection	5	15AUG07	21AUG07	136d		
0490	Start Mech System	2	11JAN08	14JAN08	36d		
0510	Trim Sprinkler System	2	08FEB08	11FEB08	15d		
0530	Final Plumbing Inspection	7	28FEB08	07MAR08	0		
0540	Final Electrical Inspection	10	18FEB08	29FEB08	5d		
0550	Final Mechanical Inspection	3	04FEB08	06FEB08	22d		
0560	Final Fire Inspection	4	27FEB08	03MAR08	4d		
0570	Final Building Inspection	10	10MAR08	21MAR08	0		
0580	CO	0		21MAR08	0		
0590	Punch/Closeout	80	24MAR08	14JUL08	0		

■ Elevator Final Inspection  
 ■ Start Mech System  
 ■ Trim Sprinkler System  
 ■ Final Plumbing Inspection  
 ■ Final Electrical Inspection  
 ■ Final Mechanical Inspection  
 ■ Final Fire Inspection  
 ■ Final Building Inspection  
 ■ CO  
 ■

Shop Drawings

Div. 02	Activity ID	Description	Original Duration	Early Start	Early Finish	Total Float	2007	2008
02-10	Trailer - Contract		5	02APR07	06APR07	23d		
02-20	Demolition - Contract		3	02APR07	04APR07	26d		
02-30	Earthwork,Paving,Drainage, S&W Service-Contract		5	02APR07	06APR07	0		
02-40	Landscaping & Sprinklers - Contract		60	02APR07	25JUN07	141d		
02-50	Surveyor - Contract		10	02APR07	13APR07	23d		
02-60	Fencing/Gates - Contract		40	02APR07	25MAY07	161d		
Div. 03								
03-10	Tilt Up Concrete - Contract		3	02APR07	04APR07	18d		
03-20	Lightweight Insulation Concrete-Contract		40	02APR07	25MAY07	90d		
Div. 05								
05-10	Structural/Railings/Mis Metals - Contract		5	02APR07	06APR07	67d		
Div. 06								
06-10	Cabinetry & Millwork- Contract		40	02APR07	25MAY07	113d		
06-20	Ext. Fram.,Metal Trusses, Sheathing-Contract		45	02APR07	04JUN07	28d		
Div. 07								

■ Trailer - Contract  
 ■ Demolition - Contract  
 ■ Earthwork,Paving,Drainage, S&W Service-Contract  
 ■ Landscaping & Sprinklers - Contract  
 ■ Surveyor - Contract  
 ■ Fencing/Gates - Contract  
 ■ Tilt Up Concrete - Contract  
 ■ Lightweight Insulation Concrete-Contract  
 ■ Structural/Railings/Mis Metals - Contract  
 ■ Cabinetry & Millwork- Contract  
 ■ Ext. Fram.,Metal Trusses, Sheathing-Contract

<b>Start date</b>	<b>02APR07</b>
<b>Finish date</b>	<b>14JUL08</b>
<b>Data date</b>	<b>02APR07</b>
<b>Page number</b>	<b>1A</b>
<b>© Primavera Systems, Inc.</b>	


**OKEEHEELEE MIDDLE SCHOOL**  
**Kaufman Lynn**  
**Baseline Schedule**


	<b>Early bar</b>
	<b>Progress bar</b>
	<b>Critical bar</b>


Activity ID	Description	Original Duration	Early Start	Early Finish	Total Float
07-10	Roofing-Contract	15	02APR07	20APR07	119d
07-20	Caulking & Waterproofing - Contract	45	02APR07	04JUN07	24d
07-30	Metal Roofing/Fascia Panels-Contract	30	02APR07	11MAY07	88d
Div. 08					
08-10	Windows - Contract	35	02APR07	18MAY07	43d
08-20	HM/Wood Doors & Frames - Contract	30	02APR07	11MAY07	144d
08-30	Finish Hardware - Contract	45	02APR07	04JUN07	129d
Div. 09					
09-10	Stucco- Contract	40	02APR07	25MAY07	118d
09-20	Drywall - Contract	15	02APR07	20APR07	109d
09-30	Ceramic Tile - Contract	30	02APR07	11MAY07	156d
09-40	Acoustical Ceiling Tile - Contract	30	02APR07	11MAY07	136d
09-50	VCT & Base - Contract	35	02APR07	18MAY07	126d
09-60	Painting - Contract	40	02APR07	25MAY07	118d
Div. 10					
10-10	Toilet Partions & Acc. - Contract	40	02APR07	25MAY07	141d
10-100	Storage Shelves - Contract	45	02APR07	04JUN07	156d
10-20	Louvers/Vents -Contract	15	02APR07	20APR07	54d
10-30	Fire Extinguisher - Contract	45	02APR07	04JUN07	166d
10-40	Tack/Marker Boards - Contract	40	02APR07	25MAY07	151d
10-50	Signage-Contract	45	02APR07	04JUN07	151d
10-60	Appliances - Contract	45	02APR07	04JUN07	171d
10-70	Corner Guards - Contract	45	02APR07	04JUN07	156d
10-80	Display Cases - Contract	45	02APR07	04JUN07	156d
10-90	Aluminum Covered Canopy-Contract	30	02APR07	11MAY07	156d
Div. 11					
11-10	Projection Screens - Contract	50	02APR07	11JUN07	146d
Div. 12					
12-10	Chemistry Lab Equipment & Casework - Contract	20	02APR07	27APR07	143d
12-20	Window Treatments - Contract	45	02APR07	04JUN07	161d
Div. 14					

**OKEEHEELEE MIDDLE SCHOOL**  
**Kaufman Lynn**  
**Baseline Schedule**

<b>Start date</b>	<b>02APR07</b>
<b>Finish date</b>	<b>14JUL08</b>
<b>Data date</b>	<b>02APR07</b>
<b>Page number</b>	<b>2A</b>
<b>© Primavera Systems, Inc.</b>	

 **Early bar**

 **Progress bar**

 **Critical bar**

Activity ID	Description	Original Duration	Early Start	Early Finish	Total Float
14-10	Elevator-Contract	10	02APR07	13APR07	136d
Div. 15					
15-10	Plumbing - Contract	11	02APR07	16APR07	39d
15-20	Mechanical -Contract	5	02APR07	06APR07	125d
15-40	Fire Sprinkler - Contract	10	02APR07	13APR07	161d
Div. 16					
16-10	Electric & Fire Alarm - Contract	5	02APR07	06APR07	13d
Div. 02					
02-12	Trailer - Prepare Shop Drawings	3	02APR07	04APR07	23d
02-22	Site Drainage - Prepare Shop Drawings	5	09APR07	13APR07	0
02-24	Site Drainage - Shop Drawing Review	10	16APR07	27APR07	0
02-32	Paving, SW, Curbing - Prepare Shop Drawings	10	09APR07	20APR07	191d
02-34	Paving, SW, Curbing - Shop Drawing Review	10	23APR07	04MAY07	191d
02-42	Landscaping & Sprinklers - Prepare Shop Drawings	10	26JUN07	10JUL07	141d
02-44	Landscaping & Sprinklers - Shop Drawing Review	10	11JUL07	24JUL07	141d
02-52	Fencing/Gates - Prepare Shop Drawings	5	29MAY07	04JUN07	161d
02-54	Fencing/Gates - Review Shop Drawings	10	05JUN07	18JUN07	161d
02-62	Soil Treatment- Prepare Shop Drawings	5	05APR07	11APR07	59d
02-64	Soil Treatment - Review Shop Drawings	10	12APR07	25APR07	59d
02-72	Sewer/Water - Prepare Shop Drawings	5	09APR07	13APR07	24d
02-74	Sewer/Water Prepare Shop Drawings	10	16APR07	27APR07	24d
Div. 03					
03-12	Concrete Mix Design - Prepare Shop Drawings	5	05APR07	11APR07	29d
03-14	Concrete Mix Design - Shop Drawing Review	10	12APR07	25APR07	29d
03-22	Rebar Foundation - Prepare Shop Drawings	5	05APR07	11APR07	41d
03-24	Rebar Foundations - Shop Drawing Review	10	12APR07	25APR07	41d
03-32	Concrete Accessories - Prepare Shop Drawings	5	05APR07	11APR07	23d
03-34	Concrete Accessories - Review Shop Drawings	10	12APR07	25APR07	23d
03-42	Tilt Panels - Prepare Shop Drawings	40	05APR07	31MAY07	18d
03-44	Tilt Panels - Shop Drawing Review	10	01JUN07	14JUN07	18d

**OKEEHEELEE MIDDLE SCHOOL**  
**Kaufman Lynn**  
**Baseline Schedule**

<b>Start date</b>	<b>02APR07</b>
<b>Finish date</b>	<b>14JUL08</b>
<b>Data date</b>	<b>02APR07</b>
<b>Page number</b>	<b>3A</b>
<b>© Primavera Systems, Inc.</b>	

**Early bar**

**Progress bar**

**Critical bar**

03-52	LW Insulating Con- Prepare Shop Drawings	5	29MAY07	04JUN07	90d	<ul style="list-style-type: none"> <li>LW Insulating Con- Prepare Shop Drawings</li> </ul>
03-54	LW Insulating Con-Review Shop Drawings	10	05JUN07	18JUN07	90d	<ul style="list-style-type: none"> <li>LW Insulating Con-Review Shop Drawings</li> </ul>
Div. 05						
05-12	Metal Roof Deck - Prepare Shop Drawings	10	09APR07	20APR07	96d	<ul style="list-style-type: none"> <li>Metal Roof Deck - Prepare Shop Drawings</li> </ul>
05-14	Metal Roof Deck - Shop Drawing Review	10	23APR07	04MAY07	96d	<ul style="list-style-type: none"> <li>Metal Roof Deck - Shop Drawing Review</li> </ul>
05-22	Stl St/Misc Metal - Prepare Shop Drawings	15	09APR07	27APR07	67d	<ul style="list-style-type: none"> <li>Stl St/Misc Metal - Prepare Shop Drawings</li> </ul>
05-24	Stl St/Misc Metal - Shop Drawing Review	10	30APR07	11MAY07	67d	<ul style="list-style-type: none"> <li>Stl St/Misc Metal - Shop Drawing Review</li> </ul>
05-32	Steel Joist -Prepare Shop Drawings	30	09APR07	18MAY07	84d	<ul style="list-style-type: none"> <li>Steel Joist -Prepare Shop Drawings</li> </ul>
05-34	Steel Joist - Review Shop Drawings	10	21MAY07	04JUN07	84d	<ul style="list-style-type: none"> <li>Steel Joist - Review Shop Drawings</li> </ul>
05-42	Steel Handrail/Metal Stair-Prepare Shop Drawings	10	09APR07	20APR07	90d	<ul style="list-style-type: none"> <li>Steel Handrail/Metal Stair-Prepare Shop Drawings</li> </ul>
05-44	Steel Handrail/Metal Stair-Review Shop Drawings	10	23APR07	04MAY07	90d	<ul style="list-style-type: none"> <li>Steel Handrail/Metal Stair-Review Shop Drawings</li> </ul>
Div. 06						
06-12	Cabinetry/Millwork-Prepare Shop Drawings	20	29MAY07	25JUN07	113d	<ul style="list-style-type: none"> <li>Cabinetry/Millwork-Prepare Shop Drawings</li> </ul>
06-14	Cabinetry/Millwork- Review Shop Drawings	10	26JUN07	10JUL07	113d	<ul style="list-style-type: none"> <li>Cabinetry/Millwork- Review Shop Drawings</li> </ul>
06-22	Ext Metal Truss/Sheathing- Prepare Shop Drawings	20	05JUN07	02JUL07	28d	<ul style="list-style-type: none"> <li>Ext Metal Truss/Sheathing- Prepare Shop Drawings</li> </ul>
06-24	Ext Metal Truss/Sheathing -Review Shop Drawings	10	03JUL07	17JUL07	28d	<ul style="list-style-type: none"> <li>Ext Metal Truss/Sheathing -Review Shop Drawings</li> </ul>
Div. 07						
07-12	Roofing -Prepare Shop Drawings	10	23APR07	04MAY07	119d	<ul style="list-style-type: none"> <li>Roofing -Prepare Shop Drawings</li> </ul>
07-14	Roofing- Review Shop Drawings	10	07MAY07	18MAY07	119d	<ul style="list-style-type: none"> <li>Roofing- Review Shop Drawings</li> </ul>
07-22	Caulking & Waterproofing- Prepare Shop Drawings	10	05JUN07	18JUN07	24d	<ul style="list-style-type: none"> <li>Caulking &amp; Waterproofing- Prepare Shop Drawings</li> </ul>
07-24	Caulking & Waterproofing - Review Shop Drawings	10	19JUN07	02JUL07	24d	<ul style="list-style-type: none"> <li>Caulking &amp; Waterproofing - Review Shop Drawings</li> </ul>
07-32	Metal Roofing/Fascia- Prepare Shop Drawing	15	14MAY07	04JUN07	88d	<ul style="list-style-type: none"> <li>Metal Roofing/Fascia- Prepare Shop Drawing</li> </ul>
07-34	Metal Roofing/Fascia - Review Shop Drawings	10	05JUN07	18JUN07	88d	<ul style="list-style-type: none"> <li>Metal Roofing/Fascia - Review Shop Drawings</li> </ul>
07-42	Insulation - Prepare Shop Drawings	5	23APR07	27APR07	146d	<ul style="list-style-type: none"> <li>Insulation - Prepare Shop Drawings</li> </ul>
07-44	Insulation - Review Shop Drawings	10	30APR07	11MAY07	146d	<ul style="list-style-type: none"> <li>Insulation - Review Shop Drawings</li> </ul>
Div. 08						
08-12	Windows- Prepare Shop Drawings	20	21MAY07	18JUN07	43d	<ul style="list-style-type: none"> <li>Windows- Prepare Shop Drawings</li> </ul>
08-14	Windows- Shop Drawing Review	10	19JUN07	02JUL07	43d	<ul style="list-style-type: none"> <li>Windows- Shop Drawing Review</li> </ul>
08-22	HM/Wood Door & Frame - Prepare Shop Drawings	10	14MAY07	25MAY07	144d	<ul style="list-style-type: none"> <li>HM/Wood Door &amp; Frame - Prepare Shop Drawings</li> </ul>
08-24	HM/Wood Door & Frame - Shop Drawing Review	10	29MAY07	11JUN07	144d	<ul style="list-style-type: none"> <li>HM/Wood Door &amp; Frame - Shop Drawing Review</li> </ul>
08-32	Finish Hardware -Prepare Shop Drawings	10	05JUN07	18JUN07	129d	<ul style="list-style-type: none"> <li>Finish Hardware -Prepare Shop Drawings</li> </ul>

**OKEEHEELEE MIDDLE SCHOOL**  
**Kaufman Lynn**  
**Baseline Schedule**

<b>Start date</b>	<b>02APR07</b>		<b>Early bar</b>
<b>Finish date</b>	<b>14JUL08</b>		<b>Progress bar</b>
<b>Data date</b>	<b>02APR07</b>		<b>Critical bar</b>
<b>Page number</b>	<b>4A</b>		
<b>© Primavera Systems, Inc.</b>			

Activity ID	Description	Original Duration	Early Start	Early Finish	Total Float
08-34	Finish Hardware-Review Shop Drawings	10	19JUN07	02JUL07	129d
Div. 09					
09-12	Stucco- Prepare Shop Drawings	5	29MAY07	04JUN07	118d
09-14	Stucco - Shop Drawing Review	10	05JUN07	18JUN07	118d
09-22	Drywall-Prepare Shop Drawings	5	23APR07	27APR07	109d
09-24	Drywall-Review Shop Drawings	10	30APR07	11MAY07	109d
09-32	Ceramic Tile -Prepare Shop Drawings	10	14MAY07	25MAY07	156d
09-34	Ceramic Tile- Review Shop Drawings	10	29MAY07	11JUN07	156d
09-42	Acoustical Tile- Prepare Shop Drawings	5	14MAY07	18MAY07	136d
09-44	Acoustical Tile - Review Shop Drawings	10	21MAY07	04JUN07	136d
09-52	VCT/Base - Prepare Shop Drawings	5	21MAY07	25MAY07	126d
09-54	VCT/Base -Review Shop Drawings	10	29MAY07	11JUN07	126d
09-62	Painting- Prepare Submittal	5	29MAY07	04JUN07	118d
09-64	Painting- Review Submittal	10	05JUN07	18JUN07	118d
Div. 10					
10-102	Storage Shelve-Prepare Shop Drawings	5	05JUN07	11JUN07	156d
10-104	Stroage Shelve-Review Shop Drawings	10	12JUN07	25JUN07	156d
10-12	Toilet Partions & Acc-Prepare Shop Drawings	10	29MAY07	11JUN07	141d
10-14	Toilet Partions & Acc-Review Shop Drawings	10	12JUN07	25JUN07	141d
10-22	Louvers/Vents - Prepare Shop Drawings	5	23APR07	27APR07	54d
10-24	Louvers/Vents-Review Shop Drawings	10	30APR07	11MAY07	54d
10-32	Fire Extingusher-Prepare Shop Drawings	5	05JUN07	11JUN07	166d
10-34	Fire Extingusher-Review Shop Drawings	10	12JUN07	25JUN07	166d
10-42	Tack/Marker Boards-Prepare Shop Drawings	10	29MAY07	11JUN07	151d
10-44	Tack/Marker Board-Review Shop Drawings	10	12JUN07	25JUN07	151d
10-52	Signage - Prepare Shop Drawings	10	05JUN07	18JUN07	151d
10-54	Signage - Review Shop Drawings	10	19JUN07	02JUL07	151d
10-62	Appliances-Prepare Shop Drawings	5	05JUN07	11JUN07	171d
10-64	Appliance- Review Shop Drawings	10	12JUN07	25JUN07	171d
10-72	Corner Guards- Prepare Shop Drawings	5	05JUN07	11JUN07	156d

**Start date 02APR07**  
**Finish date 14JUL08**  
**Data date 02APR07**  
**Page number 5A**  
 © Primavera Systems, Inc.

**OKEEHEELEE MIDDLE SCHOOL**  
**Kaufman Lynn**  
**Baseline Schedule**

**Early bar**  
**Progress bar**  
**Critical bar**

10-74	Corner Guards-Review Shop Drawings	10	12JUN07	25JUN07	156d	■ Corner Guards-Review Shop Drawings
10-82	Display Cases-Prepare Shop Drawings	5	05JUN07	11JUN07	156d	■ Display Cases-Prepare Shop Drawings
10-84	Display Case-Review Shop Drawings	10	12JUN07	25JUN07	156d	■ Display Case-Review Shop Drawings
10-92	Aluminum Canopy-Prepare Shop Drawings	5	14MAY07	18MAY07	156d	■ Aluminum Canopy-Prepare Shop Drawings
10-94	Aluminum Canopy-Review Shop Drawings	10	21MAY07	04JUN07	156d	■ Aluminum Canopy-Review Shop Drawings
Div. 11						
11-12	Projection Screens -Prepare Shop Drawings	5	12JUN07	18JUN07	146d	■ Projection Screens -Prepare Shop Drawings
11-14	Projection Screens - Review Shop Drawings	10	19JUN07	02JUL07	146d	■ Projection Screens - Review Shop Drawings
Div. 12						
12-12	Chem Lab Eq/ CW - Prepare Shop Drawings	5	30APR07	04MAY07	143d	■ Chem Lab Eq/ CW - Prepare Shop Drawings
12-14	Chem Lab Eq/ CW - Review Shop Drawings	5	07MAY07	11MAY07	143d	■ Chem Lab Eq/ CW - Review Shop Drawings
12-22	Window Treatments - Prepare Shop Drawings	5	05JUN07	11JUN07	161d	■ Window Treatments - Prepare Shop Drawings
12-24	Window Treatments - Review Shop Drawings	5	12JUN07	18JUN07	161d	■ Window Treatments - Review Shop Drawings
Div. 14						
14-12	Elevator - Prepare Shop Drawings	10	16APR07	27APR07	136d	■ Elevator - Prepare Shop Drawings
14-14	Elevator - Review Shop Drawings	10	30APR07	11MAY07	136d	■ Elevator - Review Shop Drawings
Div. 15						
15-12	Plumbing Fix- Prepare Shop Drawings	5	17APR07	23APR07	178d	■ Plumbing Fix- Prepare Shop Drawings
15-14	Plumbing Fix- Review Shop Drawings	10	24APR07	07MAY07	178d	■ Plumbing Fix- Review Shop Drawings
15-22	Plumbing Piping-Prepare Shop Drawings	5	17APR07	23APR07	39d	■ Plumbing Piping-Prepare Shop Drawings
15-24	Plumbing Piping- Review Shop Drawings	10	24APR07	07MAY07	39d	■ Plumbing Piping- Review Shop Drawings
15-32	Mechanical Eq -Prepare Shop Drawings	5	09APR07	13APR07	145d	■ Mechanical Eq -Prepare Shop Drawings
15-34	Mechanical Eq - Review Shop Drawings.	10	16APR07	27APR07	145d	■ Mechanical Eq - Review Shop Drawings.
15-42	Ductwork-Prepare Shop Drawings	20	09APR07	04MAY07	143d	■ Ductwork-Prepare Shop Drawings
15-44	Ductwork- Review Shop Drawings	10	07MAY07	18MAY07	143d	■ Ductwork- Review Shop Drawings
15-52	Fire Sprinkler - Prepare Shop Drawings	20	16APR07	11MAY07	161d	■ Fire Sprinkler - Prepare Shop Drawings
15-54	Fire Sprinkler -Review Shop Drawings	10	14MAY07	25MAY07	161d	■ Fire Sprinkler -Review Shop Drawings
15-62	Controls-Prepare Shop Drawings	10	09APR07	20APR07	145d	■ Controls-Prepare Shop Drawings
15-64	Controls- Review Shop Drawings	10	23APR07	04MAY07	145d	■ Controls- Review Shop Drawings
15-72	Chillers/Pumps/Accessories- Prepare Shop Drawings	5	09APR07	13APR07	125d	■ Chillers/Pumps/Accessories- Prepare Shop Drawings
15-74	Chillers/Pumps/Accessories-Review Shop Drawings	10	16APR07	27APR07	125d	■ Chillers/Pumps/Accessories-Review Shop Drawings

<b>Start date</b>	<b>02APR07</b>	<p align="center"><b>OKEEHEELEE MIDDLE SCHOOL</b>  <b>Kaufman Lynn</b>  <b>Baseline Schedule</b></p>		<b>Early bar</b>
<b>Finish date</b>	<b>14JUL08</b>			<b>Progress bar</b>
<b>Data date</b>	<b>02APR07</b>			<b>Critical bar</b>
<b>Page number</b>	<b>6A</b>			
<b>© Primavera Systems, Inc.</b>				

Activity ID	Description	Original Duration	Early Start	Early Finish	Total Float
Div. 16					
16-12	Conduit/Wire/Boxes- Prepare Shop Drawings	5	09APR07	13APR07	13d
16-14	Conduit/Wire/Boxes - Shop Drawing Review	10	16APR07	27APR07	13d
16-22	Fire Alarm-Prepare Shop Drawings	10	09APR07	20APR07	200d
16-24	Fire Alarm,-Review Shop Drawings	10	23APR07	04MAY07	200d
16-32	Light Fixtures-Prepare Shop Drawings	10	09APR07	20APR07	150d
16-34	Light Fixtures-Review Shop Drawings	10	23APR07	04MAY07	150d
16-42	Pis/Mcontrols/Disconnect -Prepare Shop Drawings	10	09APR07	20APR07	140d
16-44	Pis/Mcontrols/Disconnects-Review Shop Drawings	10	23APR07	04MAY07	140d
16-52	Intercom/Clock System-Prepare Shop Drawings	5	09APR07	13APR07	180d
16-54	Intercom/Clock System-Review Shop Drawings	5	16APR07	20APR07	180d
16-62	Lightning Protection-Prepare Shop Drawings	5	09APR07	13APR07	144d
16-64	Lightning Protection-Review Shop Drawings	5	16APR07	20APR07	144d
16-72	Projector Raceway System-Prepare Shop Drawings	5	09APR07	13APR07	186d
16-74	Projector Raceway System-Review Shop Drawings	5	16APR07	20APR07	186d

Div. 02					
02-16	Trailer - Deliver	3	05APR07	09APR07	23d
02-26	Site Drainage - Fab & Deliver	14	30APR07	17MAY07	0
02-36	Paving SW & Curbing Fab & Deliver	5	07MAY07	11MAY07	191d
02-46	Landscaping & Sprinklers - Fab & Deliver	5	25JUL07	31JUL07	141d
02-56	Fencing/Gates - Fab & Deliver	15	19JUN07	10JUL07	161d
02-66	Soil Treatment- Fab & Deliver	5	26APR07	02MAY07	59d
02-76	Sewer/Water-Fab & Deliver	5	30APR07	04MAY07	24d

Div. 03					
03-16	Concrete Mix Design - Fab & Deliver	2	26APR07	27APR07	29d
03-26	Rebar Foundtions - Fab & Deliver	15	26APR07	16MAY07	41d
03-36	Concrete Accessories-Order & Deliver	8	26APR07	07MAY07	23d
03-46	Tilt Panel insert/Rebar - Fab & Deliver	20	15JUN07	13JUL07	18d
03-56	Lightweight Insulating Con-Order & Deliver	20	19JUN07	17JUL07	90d

**Start date 02APR07**  
**Finish date 14JUL08**  
**Data date 02APR07**  
**Page number 7A**  
 © Primavera Systems, Inc.

**OKEEHEELEE MIDDLE SCHOOL**  
**Kaufman Lynn**  
**Baseline Schedule**

**Early bar**  
**Progress bar**  
**Critical bar**

05-16	Metal Roof Deck - Fab & Deliver	20	07MAY07	04JUN07	96d	Metal Roof Deck - Fab & Deliver
05-26	Stl St/Misc Metal - Fab & Deliver	20	14MAY07	11JUN07	67d	Stl St/Misc Metal - Fab & Deliver
05-36	Steel Joist-Fab & Deliver	5	05JUN07	11JUN07	84d	Steel Joist-Fab & Deliver
05-46	Steel Handrail/Metal Stair-Fab & Deliver	5	07MAY07	11MAY07	90d	Steel Handrail/Metal Stair-Fab & Deliver
Div. 06						
06-16	Cabinetry/Millwork -Fab & Deliver	30	11JUL07	21AUG07	113d	Cabinetry/Millwork -Fab & Deliver
06-26	Ext Metal Trusses/Sheathing- Fab & Deliver	50	18JUL07	26SEP07	28d	Ext Metal Trusses/Sheathing- Fab & Deliver
Div. 07						
07-16	Roofing -Fab & Deliver	15	21MAY07	11JUN07	119d	Roofing -Fab & Deliver
07-26	Caulking/Waterproofing - Fab & Deliver	10	03JUL07	17JUL07	24d	Caulking/Waterproofing - Fab & Deliver
07-36	Metal Roofing/Fascia-Fab-Deliver	10	19JUN07	02JUL07	88d	Metal Roofing/Fascia-Fab-Deliver
07-46	Insulation-Order & Deliver	5	14MAY07	18MAY07	146d	Insulation-Order & Deliver
Div. 08						
08-16	Windows-Fab & Deliver	40	03JUL07	28AUG07	43d	Windows-Fab & Deliver
08-26	HM/Wood Door & Frame - Fab & Deliver	30	12JUN07	24JUL07	144d	HM/Wood Door & Frame - Fab & Deliver
08-46	Finish Hardware-Fab & Deliver	30	03JUL07	14AUG07	129d	Finish Hardware-Fab & Deliver
Div. 09						
09-16	Stucco-Fab & Deliver	5	19JUN07	25JUN07	118d	Stucco-Fab & Deliver
09-26	Drywall-Fab & Deliver	5	14MAY07	18MAY07	109d	Drywall-Fab & Deliver
09-36	Ceramic Tile - Fab & Deliver	15	12JUN07	02JUL07	156d	Ceramic Tile - Fab & Deliver
09-46	Acoustical Tile- Fab & Deliver	15	05JUN07	25JUN07	136d	Acoustical Tile- Fab & Deliver
09-56	VCT/Base -Fab & Deliver	30	12JUN07	24JUL07	126d	VCT/Base -Fab & Deliver
09-66	Painting -Fab & Deliver	15	19JUN07	10JUL07	118d	Painting -Fab & Deliver
Div. 10						
10-106	Storage Shelves-Order & Deliver	15	26JUN07	17JUL07	156d	Storage Shelves-Order & Deliver
10-16	Toilet Partions & Acc.-Fab & Deliver	30	26JUN07	07AUG07	141d	Toilet Partions & Acc.-Fab & Deliver
10-26	Louvers/Vents-Order & Deliver	15	14MAY07	04JUN07	54d	Louvers/Vents-Order & Deliver
10-36	Fire Extingusher-Order & Deliver	10	26JUN07	10JUL07	166d	Fire Extingusher-Order & Deliver
10-46	Tack/Marker Boards- Fab & Deliver	20	26JUN07	24JUL07	151d	Tack/Marker Boards- Fab & Deliver
10-56	Signage- Fab & Deliver	20	03JUL07	31JUL07	151d	Signage- Fab & Deliver
10-66	Appliance-order & Deliver	5	26JUN07	02JUL07	171d	Appliance-order & Deliver

**Start date 02APR07**  
**Finish date 14JUL08**  
**Data date 02APR07**  
**Page number 8A**  
 © Primavera Systems, Inc.

**OKEEHEELEE MIDDLE SCHOOL**  
**Kaufman Lynn**  
**Baseline Schedule**

Early bar  
 Progress bar  
 Critical bar



10-76	Corner Guards-Fab & Deliver	20	26JUN07	24JUL07	156d	■ Corner Guards-Fab & Deliver
10-86	Display Case-Order Deliver	20	26JUN07	24JUL07	156d	■ Display Case-Order Deliver
10-96	Aluminum Canopy-Fab & Deliver	30	05JUN07	17JUL07	156d	■ Aluminum Canopy-Fab & Deliver
Div. 11						
11-16	Protection Screens-Order & Deliver	20	03JUL07	31JUL07	146d	■ Protection Screens-Order & Deliver
Div. 12						
12-16	Chem Lab Eq/Casework-Fab & Deliver	40	14MAY07	10JUL07	143d	■ Chem Lab Eq/Casework-Fab & Deliver
12-26	Window Treatments-Order & Deliver	15	19JUN07	10JUL07	161d	■ Window Treatments-Order & Deliver
Div. 14						
14-16	Elevator - Fab. & Deliver	40	14MAY07	10JUL07	136d	■ Elevator - Fab. & Deliver
Div. 15						
15-16	Plumbing Fix-Fab & Deliver	20	08MAY07	05JUN07	178d	■ Plumbing Fix-Fab & Deliver
15-26	Plumbing Piping-Fab & Deliver	10	08MAY07	21MAY07	39d	■ Plumbing Piping-Fab & Deliver
15-36	Mechanical Eq Ex Fans, Etc Fab & Deliver	20	30APR07	25MAY07	145d	■ Mechanical Eq Ex Fans, Etc Fab & Deliver
15-46	Duckwork-Fab & Deliver	20	21MAY07	18JUN07	143d	■ Duckwork-Fab & Deliver
15-56	Fire Sprinkler-Fab & Deliver	10	14MAY07	25MAY07	161d	■ Fire Sprinkler-Fab & Deliver
15-66	Controls-Fab & Deliver	15	07MAY07	25MAY07	145d	■ Controls-Fab & Deliver
15-76	Chillers/Pumps/Accessories-Fab & Deliver	40	30APR07	25JUN07	125d	■ Chillers/Pumps/Accessories-Fab & Deliver
Div. 16						
16-16	Conduits/Wire/Boxes - Fab & Deliver	5	30APR07	04MAY07	13d	■ Conduits/Wire/Boxes - Fab & Deliver
16-26	Fire Alarm-Fab & Deliver	30	02APR07	11MAY07	195d	■ Fire Alarm-Fab & Deliver
16-36	Light fixtures-Fab & Deliver	40	07MAY07	02JUL07	150d	■ Light fixtures-Fab & Deliver
16-46	Pls/Mcontrols/Disconnects-Fab & Deliver	30	02APR07	11MAY07	135d	■ Pls/Mcontrols/Disconnects-Fab & Deliver
16-56	Intercom/Clock System-Fab & Deliver	30	23APR07	04JUN07	180d	■ Intercom/Clock System-Fab & Deliver
16-66	Lightning Protection-Fab & Deliver	10	23APR07	04MAY07	144d	■ Lightning Protection-Fab & Deliver
16-76	Projector Raceway System-Fab & Deliver	30	23APR07	04JUN07	186d	■ Projector Raceway System-Fab & Deliver

Site Work

0017	Site Demolition	5	10APR07	16APR07	23d	■ Site Demolition
0018	Lavout Building Control Points	1	16APR07	16APR07	23d	■ Lavout Building Control Points
0019	Drainage System at South Side of Blding	5	18MAY07	24MAY07	0	■ Drainage System at South Side of Blding

**Start date 02APR07**  
**Finish date 14JUL08**  
**Data date 02APR07**  
**Page number 9A**  
 © Primavera Systems, Inc.

**OKEEHEELEE MIDDLE SCHOOL**  
**Kaufman Lynn**  
**Baseline Schedule**

Early bar  
 Progress bar  
 Critical bar

Activity ID	Description	Original Duration	Early Start	Early Finish	Total Float
0020	Drainage System on North Side of Blding	5	25MAY07	01JUN07	0
0021	Install New Sewer line	5	04JUN07	08JUN07	159d
0022	Install Water Service	3	11JUN07	13JUN07	159d
0023	Install new Fire Line	7	14JUN07	22JUN07	159d
0025	Cut & Balance Site/Building Pad	3	04JUN07	06JUN07	0
0033	Install Electrical Ductbank	9	07MAY07	17MAY07	13d
0034	Install Underground Chiller lines	10	28SEP07	11OCT07	69d
0035	Grade Site	3	11FEB08	13FEB08	2d
0045	Install Side Walks	10	14FEB08	27FEB08	2d
0135	Install Landscaping	10	21FEB08	05MAR08	2d
0136	Install Fence and Gates	5	28FEB08	05MAR08	2d
0145	Install Irrigation System	10	21FEB08	05MAR08	2d
0146	Install Aluminum Covered Walkway	5	28FEB08	05MAR08	2d

Activity ID	Description	Original Duration	Early Start	Early Finish	Total Float
0030	Layout Foundations	2	07JUN07	08JUN07	0
0031	Excavate Elevator Pit Foundations	1	11JUN07	11JUN07	0
0032	Excavate Perimeter Foundations	7	12JUN07	20JUN07	0
0036	Excavate Interior Column Foundations	6	21JUN07	28JUN07	0
0040	Excavate Stair Foundations	7	29JUN07	10JUL07	0
0041	Excavate Chiller Building Foundations	2	11JUL07	12JUL07	3d
0042	Form/Rebar Elevator Pit Foundations	2	11JUN07	12JUN07	25d
0043	Form/Rebar Perimeter Foundations	10	14JUN07	27JUN07	8d
0044	Form/Place Rebar Interior Column Foundations	7	28JUN07	09JUL07	6d
0046	Form/Place Rebar Stair Foundations	5	11JUL07	17JUL07	0
0047	Form/PlaceRebar Chiller Building Foundations	3	13JUL07	17JUL07	3d
0050	Inspect and Pour Elevator Pit Foundation	2	13JUN07	14JUN07	25d
0051	Inspect and Pour Perimeter Foundation	10	21JUN07	05JUL07	8d
0052	Inspect and Pour Interior Column Foundations	5	10JUL07	16JUL07	6d
0053	Inspect and Pour Stair Foundations	5	18JUL07	24JUL07	0

**Start date 02APR07**  
**Finish date 14JUL08**  
**Data date 02APR07**  
**Page number 10A**  
 © Primavera Systems, Inc.

**OKEEHEELEE MIDDLE SCHOOL**  
**Kaufman Lynn**  
**Baseline Schedule**

**Early bar**  
**Progress bar**  
**Critical bar**

Activity ID	Description	Original Duration	Early Start	Early Finish	Total Float
0054	Inspect and Pour Chiller Building Foundation	2	18JUL07	19JUL07	3d
080	Form, Place Rebar Elevator Pit Walls	1	15JUN07	15JUN07	25d
082	Inspect and pour Elevator Pit Walls	2	15JUN07	18JUN07	25d
091	SOG Mechanical Rough	3	06JUL07	10JUL07	10d
0120	SOG Plumbing Rough	5	06JUL07	12JUL07	8d
0130	SOG Electrical Rough	5	06JUL07	12JUL07	8d
0131	Backfill and compact Subgrade	4	25JUL07	30JUL07	0
0140	Soil Poisoning	2	27JUL07	30JUL07	0
0141	Under slab vaporbarrier	2	30JUL07	31JUL07	0
0142	SOG Reinforcing	4	31JUL07	03AUG07	0
0150	Inspect/Pour Slab on Grade	3	06AUG07	08AUG07	0
0160	Form/place rebar-inserts-South side Panels	7	09AUG07	17AUG07	0
0162	Inspect/Pour-South side Panels	4	15AUG07	20AUG07	0
0163	Brace/Weld South Side Panels	4	21AUG07	24AUG07	0
0164	Form/place rebar-insert-North side Panels	7	27AUG07	05SEP07	0
0170	Inspect/Pour-North side Panels	3	06SEP07	10SEP07	0
0171	Brace/Weld North side Panels	4	11SEP07	14SEP07	0
0172	Form/place rebar-inserts-Chiller Building	3	17SEP07	19SEP07	59d
0173	Inspect/Pour -Chiller Building Panels	4	20SEP07	25SEP07	59d
0174	Brace/Weld Chiller Building Panel	2	26SEP07	27SEP07	59d
0180	Install Structural Steel Columns	3	17SEP07	19SEP07	0
0182	Install Structural Steel floor Beams	5	20SEP07	26SEP07	0
0184	Install 2nd Floor Metal Deck	7	18SEP07	26SEP07	0
0185	Install Stair/Handrails	5	18SEP07	24SEP07	2d
0190	Plumbing Rough-2nd Floor	5	20SEP07	26SEP07	0
0200	Electrical Rough - 2nd Floor	5	20SEP07	26SEP07	0
0210	Mechanical Rough - 2nd Floor	5	19SEP07	26SEP07	1d
0220	Place Rebar-2nd Floor	4	27SEP07	02OCT07	0

- Inspect and Pour Chiller Building Foundation
- Form, Place Rebar Elevator Pit Walls
- Inspect and pour Elevator Pit Walls
- SOG Mechanical Rough
- SOG Plumbing Rough
- SOG Electrical Rough
- Backfill and compact Subgrade
- Soil Poisoning
- Under slab vaporbarrier
- SOG Reinforcing
- Inspect/Pour Slab on Grade
- Form/place rebar-inserts-South side Panels
- Inspect/Pour-South side Panels
- Brace/Weld South Side Panels
- Form/place rebar-insert-North side Panels
- Inspect/Pour-North side Panels
- Brace/Weld North side Panels
- Form/place rebar-inserts-Chiller Building
- Inspect/Pour - Chiller Building Panels
- Brace/Weld Chiller Building Panel
- Install Structural Steel Columns
- Install Structural Steel floor Beams
- Install 2nd Floor Metal Deck
- Install Stair/Handrails
- Plumbing Rough-2nd Floor
- Electrical Rough - 2nd Floor
- Mechanical Rough - 2nd Floor
- Place Rebar-2nd Floor

**Start date** 02APR07

**Finish date** 14JUL08

**Data date** 02APR07

**Page number** 11A

© Primavera Systems, Inc.

**OKEEHEELEE MIDDLE SCHOOL**  
Kaufman Lynn  
Baseline Schedule

**Early bar**

**Progress bar**

**Critical bar**

Activity ID	Description	Original Duration	Early Start	Early Finish	Total Float
0230	Inspect/ Pour 2nd Floor	3	03OCT07	05OCT07	0
0240	Install Roof Beams	2	08OCT07	09OCT07	0
0242	Install Roof Joist	10	10OCT07	23OCT07	0
0350	Install MetalRoof Decking	7	17OCT07	25OCT07	2d
0360	MEP Rough Roof Deck	3	19OCT07	23OCT07	19d
0370	Inspect Metal Roof Deck	2	26OCT07	29OCT07	17d

Activity ID	Description	Original Duration	Early Start	Early Finish	Total Float
01-010	Interior Wall Framing First Fl.	10	24OCT07	06NOV07	0
01-019	Hang First Fl Ductwork	15	31OCT07	20NOV07	49d
01-020	Install Interior Window Frames	2	07NOV07	08NOV07	20d
01-030	Install Waste & Vents First Fl	3	30OCT07	01NOV07	17d
01-050	Install Plumbing Wall/Ceiling Rough First Fl	7	02NOV07	12NOV07	17d
01-060	Install Electrical Wall/Ceiling Rough First Fl	10	02NOV07	15NOV07	14d
01-070	Install Sprinkler Ceiling Rough First Fl	10	02NOV07	15NOV07	50d
01-080	Plumbing Close In Inspection First Fl	1	13NOV07	13NOV07	17d
01-090	Mechanical Close In Inspection First Fl	1	21NOV07	21NOV07	49d
01-100	Electrical Close In Inspection First Fl	1	16NOV07	16NOV07	14d
01-120	Sprinkler Close In Inspections First Fl	1	16NOV07	16NOV07	50d
01-121	Building Close In Inspection First Fl	1	16NOV07	16NOV07	14d
01-140	Hang Drywall Partitions First Fl	10	19NOV07	04DEC07	14d
01-141	Install Insulation First FL	5	28NOV07	04DEC07	14d
01-145	Insulation Inspection First Fl	2	03DEC07	04DEC07	14d
01-150	Screw Inspection First Fl	2	05DEC07	06DEC07	14d
01-151	Finish Drywall Partitions First Fl	10	07DEC07	20DEC07	14d
01-152	Frame Drywall Ceilings First Fl	3	14DEC07	18DEC07	26d
01-153	MEP Ceiling Rough-DW Ceilings -First Fl	4	19DEC07	26DEC07	26d
01-154	Above Ceiling Inspection -First Fl	2	27DEC07	28DEC07	26d
01-155	Hang DW Ceilings - First Fl	3	02JAN08	04JAN08	26d
01-156	Screw Inspection DW Ceiling First Fl	2	07JAN08	08JAN08	26d

**Start date 02APR07**  
**Finish date 14JUL08**  
**Data date 02APR07**  
**Page number 12A**  
 © Primavera Systems, Inc.

**OKEEHEELEE MIDDLE SCHOOL**  
**Kaufman Lynn**  
**Baseline Schedule**

**Early bar**  
**Progress bar**  
**Critical bar**

Activity ID	Description	Total Duration	Early Start	Early Finish	Total Floor
01-157	Finish DW Ceiling -First FI	5	09JAN08	15JAN08	26d
01-161	Install Ceramic Tile-First FL	10	11JAN08	24JAN08	26d
01-171	Paint Primer Walls First FI	5	14DEC07	20DEC07	14d
01-210	Install Ceiling Grid First FI	5	19DEC07	27DEC07	14d
01-211	Finish Coat of Paint -First FI	10	28DEC07	14JAN08	14d
01-220	Install Flex Duct and Grilles First FI	5	26DEC07	03JAN08	15d
01-225	Start-UP HVAC	1	04JAN08	04JAN08	15d
01-230	Install Light Fixtures and Trim First FI	10	26DEC07	10JAN08	30d
01-239	Install VCT/Rubber Base-First FI	15	08JAN08	28JAN08	14d
01-240	Install Cabinets/Millwork- First Floor	15	17JAN08	06FEB08	14d
01-245	Install Door & Hardware-First FI	5	01FEB08	07FEB08	14d
01-250	Center Sprinkler Heads-First FI	4	26DEC07	02JAN08	43d
01-260	Install Plumbing Fixtures First FI	5	22JAN08	28JAN08	22d
01-270	Above Ceiling Inspection -First FI	2	11JAN08	14JAN08	34d
01-280	Install Ceiling Tiles-First FI	5	15JAN08	21JAN08	34d
01-290	Install FA/Intercom/Cliks Devices-First FI	7	11JAN08	21JAN08	30d
01-300	Install Toilet Part/Access First FI	5	25JAN08	31JAN08	26d
01-310	Install Tack/Mker/Proj Scr/Tables First FI	5	15JAN08	21JAN08	34d

02-010	Interior Framing Second FI.	10	14NOV07	29NOV07	0
02-019	Hang Ductwork Second FI	15	21NOV07	13DEC07	34d
02-020	Install Waste & Vents Second FI	3	30NOV07	04DEC07	7d
02-050	Install Plumbing Wall/Ceiling Rough Second FI	7	30NOV07	10DEC07	3d
02-060	Install Electrical Wall/Ceiling Rough Second FI	10	30NOV07	13DEC07	0
02-070	Install Sprinkler Ceiling Rough Second FI	10	30NOV07	13DEC07	34d
02-080	Plumbing Close In Inspection Second FI	1	11DEC07	11DEC07	3d
02-090	Mechanical Close In Inspection Second FI	1	14DEC07	14DEC07	34d
02-100	Electrical Close In Inspection Second FI	1	14DEC07	14DEC07	0
02-109	Sprinkler Close In Inspections Second FI	1	14DEC07	14DEC07	34d

**Start date** 02APR07  
**Finish date** 14JUL08  
**Data date** 02APR07  
**Page number** 13A  
 © Primavera Systems, Inc.

**OKEEHEELEE MIDDLE SCHOOL**  
**Kaufman Lynn**  
**Baseline Schedule**

**Early bar**  
**Progress bar**  
**Critical bar**

Activity ID	Description	Original Duration	Early Start	Early Finish	Total Float	2007	2008
02-110	Building Close In Inspection Second FI	1	14DEC07	14DEC07	0		
02-140	Hang Drywall Second FI	10	17DEC07	03JAN08	0		
02-141	Install Insulation Second FI	5	04JAN08	10JAN08	0		
02-142	Insulation Inspection Second FI	2	11JAN08	14JAN08	0		
02-150	Screw Inspection Second FI	1	15JAN08	15JAN08	0		
02-151	Finish Drywall Second FI	10	16JAN08	29JAN08	0		
02-161	Frame Drywall Ceilings Second FI	3	23JAN08	25JAN08	2d		
02-162	MEP Ceiling Rough-DW Ceilings Second FI	4	28JAN08	31JAN08	2d		
02-163	Above Ceiling Inspection Second FI	2	01FEB08	04FEB08	2d		
02-164	Hang DW Ceilings Second FI	3	05FEB08	07FEB08	2d		
02-165	Screw Inspection DW Ceilings Second FI	2	08FEB08	11FEB08	2d		
02-166	Finish DW Ceilings Second FI	5	12FEB08	18FEB08	2d		
02-167	Install Ceramic Tile Second FI	10	14FEB08	27FEB08	2d		
02-170	Prime Paint Second FI	5	23JAN08	29JAN08	0		
02-180	Install Ceiling Grid Second FI	5	28JAN08	01FEB08	0		
02-190	Final Coat Paint Second FI	10	04FEB08	15FEB08	0		
02-220	Install Flex Duct & Grilles - Second FI	5	28JAN08	01FEB08	4d		
02-221	Start Up- HVAC Second FI	1	04FEB08	04FEB08	4d		
02-230	Install Light Fixtures & Trim Second FI.	10	04FEB08	15FEB08	4d		
02-231	Install VCT/Rubber Base Second FI	5	11FEB08	15FEB08	0		
02-232	Install Cabinets/Millwork Second FI	15	18FEB08	07MAR08	0		
02-245	Install Door & Hardware Second FI	5	21FEB08	27FEB08	0		
02-250	Center Sprinkler Heads Second FI	4	04FEB08	07FEB08	14d		
02-260	Install Plumbing Fixtures Second FI	5	21FEB08	27FEB08	0		
02-270	Above Ceiling Inspection Second FI	2	18FEB08	19FEB08	8d		
02-280	Install Ceiling Tile-Second FI	5	20FEB08	26FEB08	8d		
02-290	Install FA/Intercom/Clks Devices - Second FI	7	18FEB08	26FEB08	4d		
02-300	Install Toilet Part/ Access Second FI	5	28FEB08	05MAR08	2d		
02-310	Install Tack/Mker/Proj Scr/Tables Second FI	5	18FEB08	22FEB08	10d		

**Start date 02APR07**  
**Finish date 14JUL08**  
**Data date 02APR07**  
**Page number 14A**  
 © Primavera Systems, Inc.

**OKEEHEELEE MIDDLE SCHOOL**  
**Kaufman Lynn**  
**Baseline Schedule**

**Early bar**  
**Progress bar**  
**Critical bar**

Activity ID	Description	Original Duration	Early Start	Early Finish	Total Float
0450	Install Rails and Cab	20	11JUL07	07AUG07	136d
0460	Start Up Elevator	5	08AUG07	14AUG07	136d
<b>Exterior</b>					
0386	Set Chillers,Pumps & Piping @ Chiller Building	10	28SEP07	11OCT07	59d
0387	Set AHUs/Mech Rm Fit out- First FL	5	12OCT07	18OCT07	59d
0388	Set AHUs/Mech Rm Fit out- Second FL	5	19OCT07	25OCT07	59d
0391	Install Lightweight Insulating Concrete on Roof	4	30OCT07	02NOV07	17d
0392	Dry In Roof	7	05NOV07	13NOV07	17d
0393	Install Exterior Alum Windows	15	26OCT07	15NOV07	2d
0394	Install Ext Metal Trusses,Sheathing & Framing	18	02NOV07	29NOV07	2d
0395	Install Metal Roofing and Side	15	16NOV07	10DEC07	2d
0396	Frame Exterior Soffits	5	11DEC07	17DEC07	2d
0397	Inspect Framing	2	18DEC07	19DEC07	2d
0398	Stucco Exterior Soffits	5	20DEC07	28DEC07	2d
0400	Clean Thin Brick & Seal	15	02JAN08	22JAN08	2d
0410	Paint Exterior of Building	20	23JAN08	19FEB08	2d

**Start date** 02APR07

**Finish date** 14JUL08

**Data date** 02APR07

**Page number** 15A

© Primavera Systems, Inc.

**OKEEHEELEE MIDDLE SCHOOL**  
**Kaufman Lynn**  
**Baseline Schedule**

**Early bar**

**Progress bar**

**Critical bar**

TAB 11





**Okeehelée Middle School Classroom Additions  
2200 Pinehurst Drive  
Greenacres, Florida 33413  
SDPBC Project No. 2151-8307  
February 1, 2007**

## **Value Engineering**

### **Cost Savings Ideas Implemented**

- 1 Utilize an 8" limerock base covered in sod in lieu of Turf Block Pavers at the emergency access road.
- 2 Utilize the close proximity of the existing underground utilities for utility tie-ins in lieu of running all new services.
- 3 Utilize tilt wall construction for the main building and chiller yard enclosure in lieu of conventional concrete and masonry structure.
- 4 Deleting the brick and form liner work at the 13 "typical" window areas as shown on the attached SK-1.
- 5 Utilizing 24-gauge metal fascia and 22-gauge metal roofing in lieu of using 22-gauge throughout.
- 6 Utilize a single corridor layout for the main building floor plan.
- 7 Routing of the electrical service to the chiller yard first in lieu of running it to the building's main electrical room and then back out to the chiller.

### **Cost Savings Ideas That Were Not Implemented**

- 1 Delete the thin-brick work in its entirety. This was rejected so as to keep a similar look as the existing adjacent classroom buildings.
- 2 Deleting the wire mesh requirement in the Light Weight Insulating Concrete.
- 3 Deleting the 350 PSI Lightweight Concrete requirement and using a 200 PSI product.

622 Banyan Trail ♦ Suite 300 ♦ Boca Raton, Florida 33431 ♦ Phone (561) 361-6700 ♦ Fax (561) 361-6979

GREATER BOCA RATON CHAMBER OF COMMERCE  
**BUSINESS OF THE YEAR 2005**  
[www.kaufmanlynn.com](http://www.kaufmanlynn.com) ♦ CGC# 021732

4. Deleting all of the metal fascia work. This was rejected so as to keep a similar look as the existing adjacent classroom buildings.
5. Deleting the epoxy grout requirement for the tile at the restrooms. This was rejected due to maintenance issues
6. Using an alternate ceiling tile material. This was rejected due to maintenance/replace-ability issues
7. Delete the acoustical ceilings in the classrooms and utilize an "open air" scenario.
8. Relocating the chiller yard enclosure closer to the classroom building. The reason this was rejected was that putting the enclosure too close to the building could cause problems with noise in the classrooms.
9. Deleting the acoustical wall panels at the chiller yard. The reason this was rejected was that deleting these may increase the noise factor too much for the classrooms
